


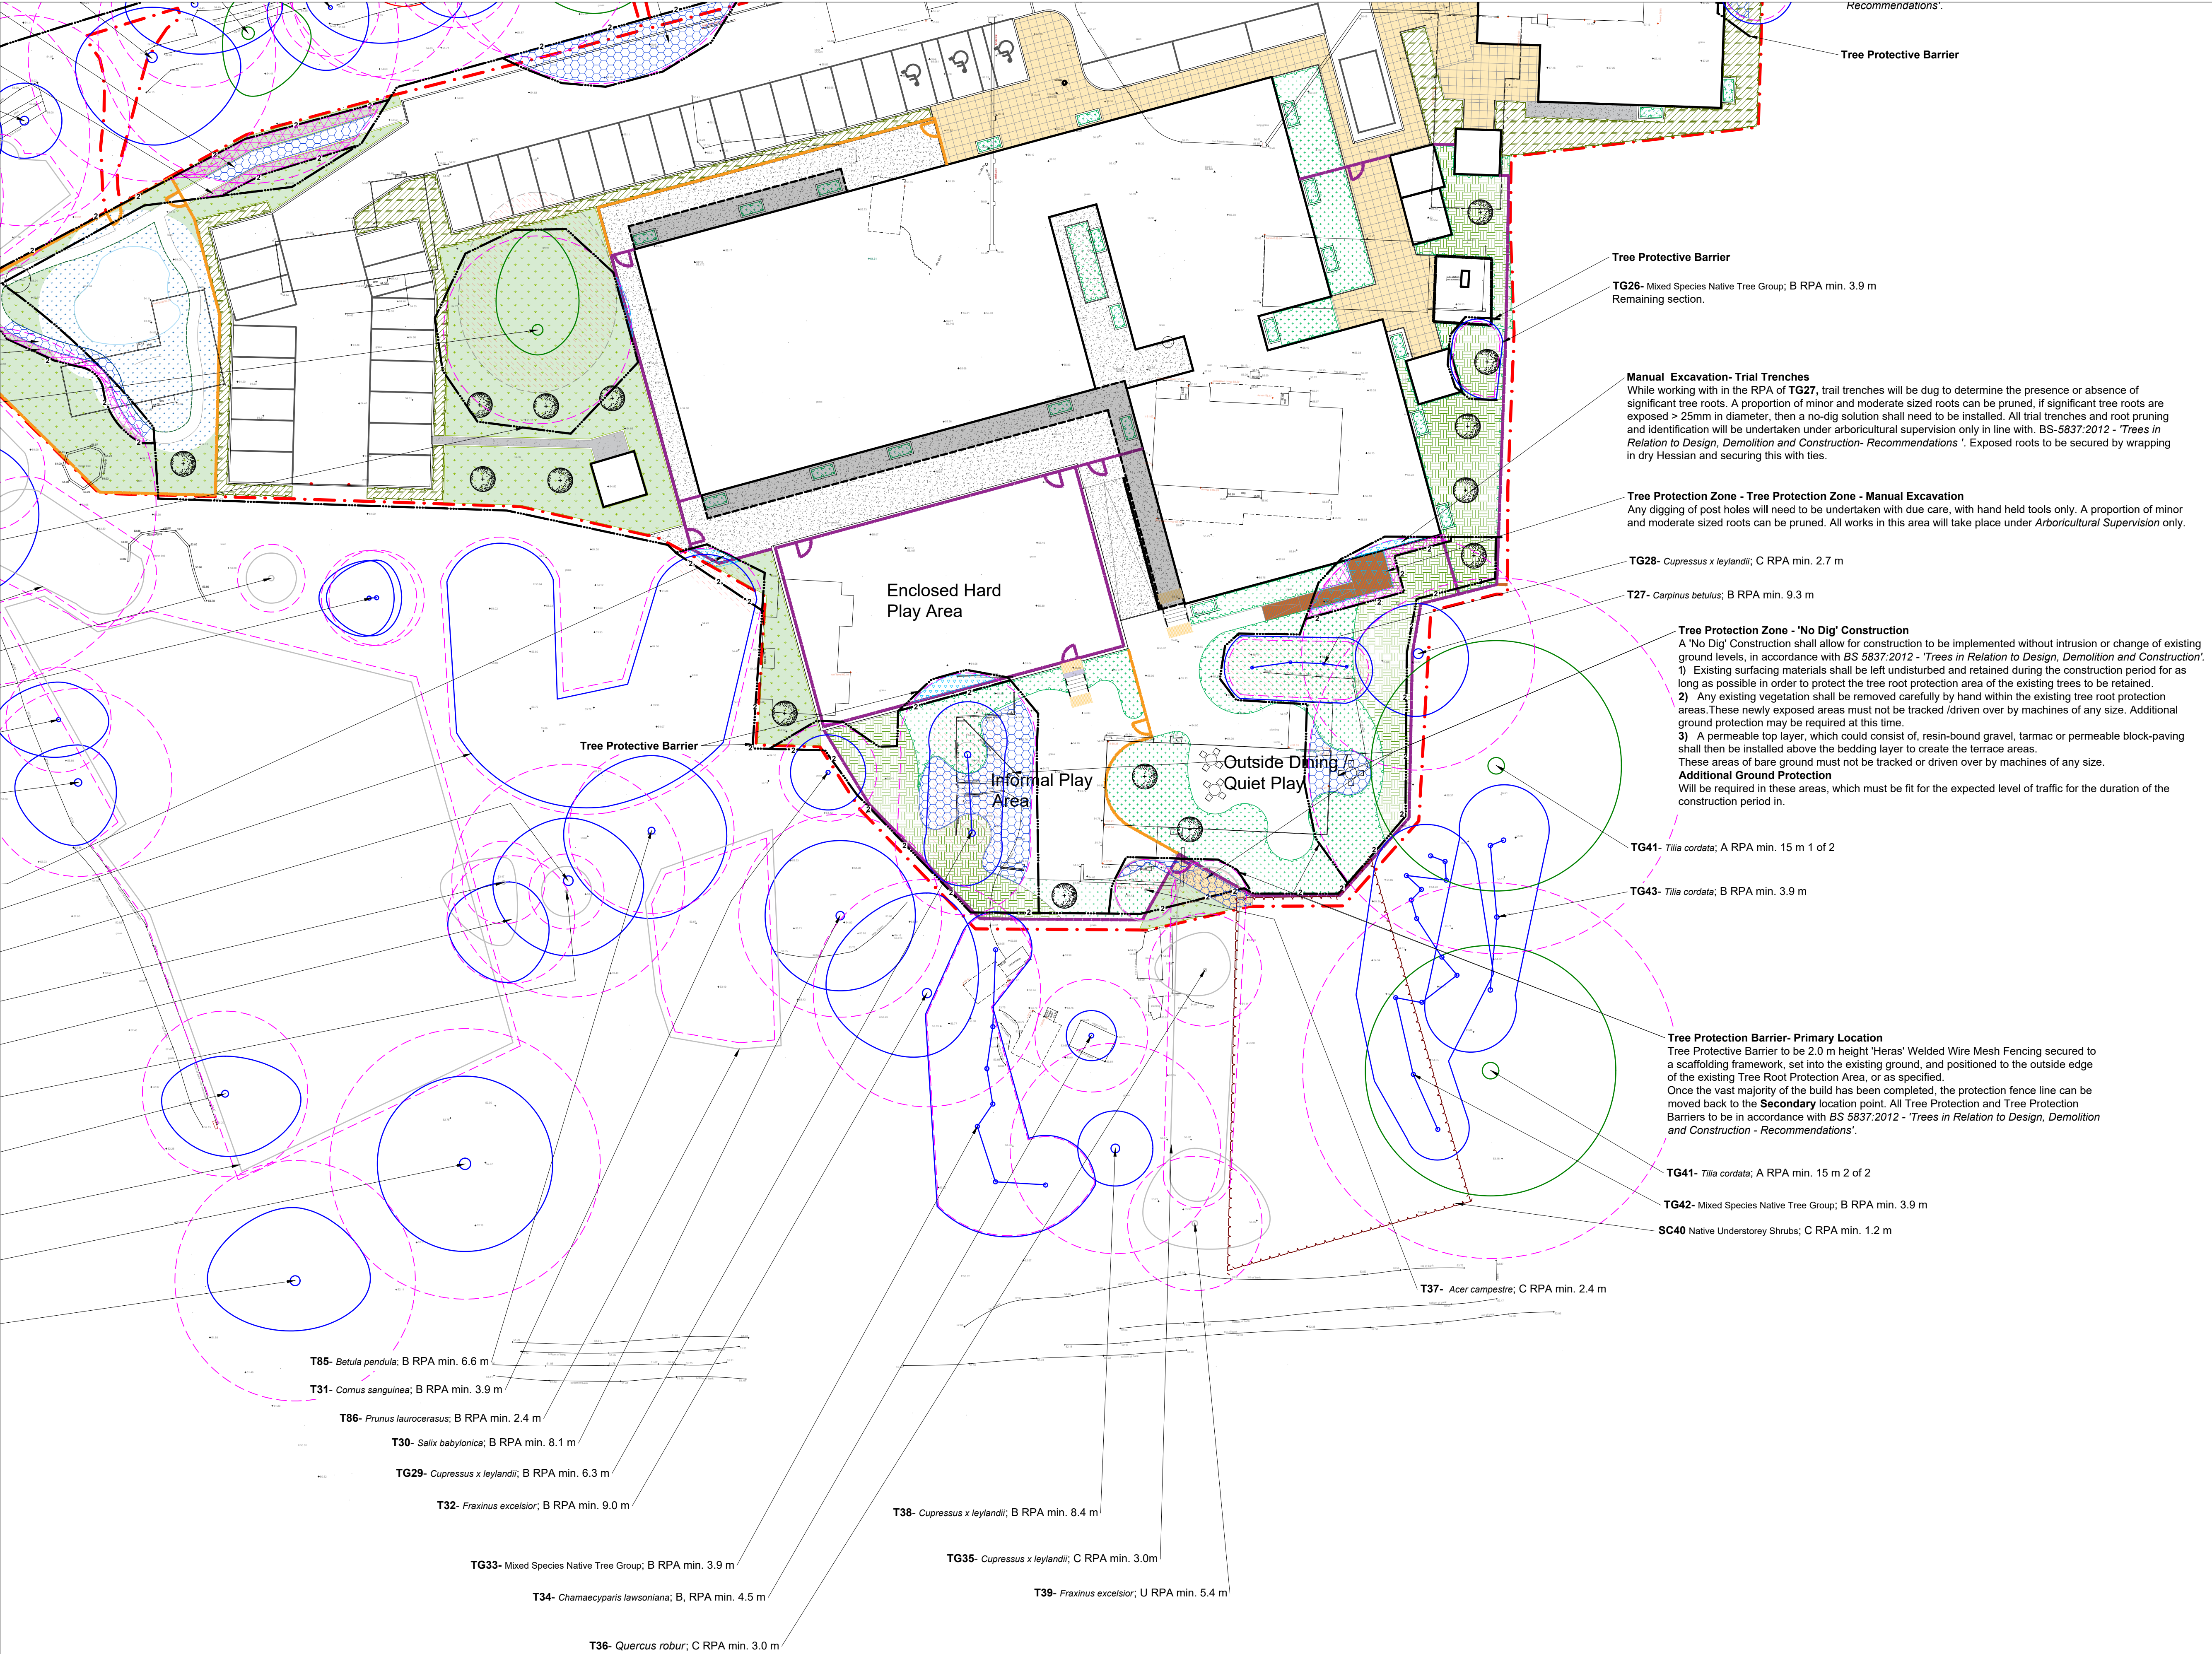

Legend

- T02 Tree, Hedgerow and Shrub Numbers.**
- Tree Root Protection Areas**
Specified in accordance with BS 5837:2012 - 'Trees in Relation to Design, Demolition and Construction - Recommendations'.
- Category A Trees**
Trees of High Quality and Value to be Retained.
- Category B Trees**
Trees of Moderate Quality and Value to be Retained.
- Category C Trees**
Trees of Low Quality and Value to be Retained.
- Category U Trees**
Trees unsuitable for long term retention.
- Existing Trees to be Removed**
All operations to be in accordance with BS3998:2010- 'Tree Works- Recommendations'
- Existing Shrubs and Hedges to be Removed**

- Tree Protection Barrier**
All Tree Protection Barriers to be in accordance with BS 5837:2012 - 'Trees in Relation to Design, Demolition and Construction - Recommendations'.
2.0 m height 'Heras' Welded Wire Mesh Fencing secured and positioned as specified.
- 2nd Location- Tree Protection Barrier**
This is the secondary location of the protection fencing. Once the vast majority of the build has been completed, the protection fence line can be moved back to this point to allow the implementation of Soft Landscaping.

- Protection Zone - 'No Dig' Construction**
Works to be implemented without intrusion or change of existing ground levels, in accordance with BS 5837:2012 - 'Trees in Relation to Design, Demolition and Construction - Recommendations'.

- Protection Zone - Operation Zone During Construction.**
An Operation Zone shall be implemented within the Root Protection Area. Ground protection, fit for the expected level of traffic, shall be secured for the duration of the construction period in accordance with BS 5837:2012 - 'Trees in Relation to Design, Demolition and Construction - Recommendations'.

- Protection Zone - Manual Excavation**
A Limited Manual Excavation shall be implemented, in accordance with BS 5837:2012 - 'Trees in Relation to Design, Demolition and Construction - Recommendations'. All works in these areas shall be undertaken with due care with hand held tools under Arboricultural Supervision only.

- Notes:
- Drawing to be read in colour.
 - For details of existing trees and vegetation refer to: LLD3660-ARB-SCH-001 - Existing Tree Schedule;
 - For assessment of effects of the proposed development on existing trees refer to LLD3660-ARB-REP-001- Arboricultural Impact Assessment and Method Statement.

PLANNING ISSUE

Rev	Description	Date	Initials
03	Planning Issue	13.03.26	GO
02	Draft Issue	13.01.26	RM
01	Draft Issue	08.01.26	GO
00	Draft Issue	06.01.26	GO

 **LIZARD**
Landscape Design and Ecology
The Old Bank, 34 South Street, Tarring, Worthing, West Sussex, BN14 7LH
T. 01903 216033 E. lizardlandscape@btconnect.com W. lizardlandscape.co.uk

Client Salutem Shared Services			
Project Title and Location Woodview School on Ingfield Manor School. Manor Drive, Five Oaks, Billingshurst RH14 9AX			
Drawing Title Tree Retention and Protection Plan			
Scale 1:250@A1	Drawn GO	Approved KM	Date 06/01/2026
Drawing No LLD3660-ARB-DWG-022			Revision 03

Tree Retention and Protection Plan
South Side- Ingfield Manor Drive, Five Oaks, Billingshurst RH14 9AX
