


CONSTRUCT dwelling within footprint; driveway (permeable, no-dig if encroaching) and foul/surface-water services kept clear of RPAs; barriers retained until completion.

Surface-water route (dashed) & foul route (dotted) taken clear of the RPAs to the flow-control chamber, package treatment plant and eastern outfalls (read with drainage drawing 1048_1001). Permeable driveway kept clear of RPAs; no-dig if encroaching.

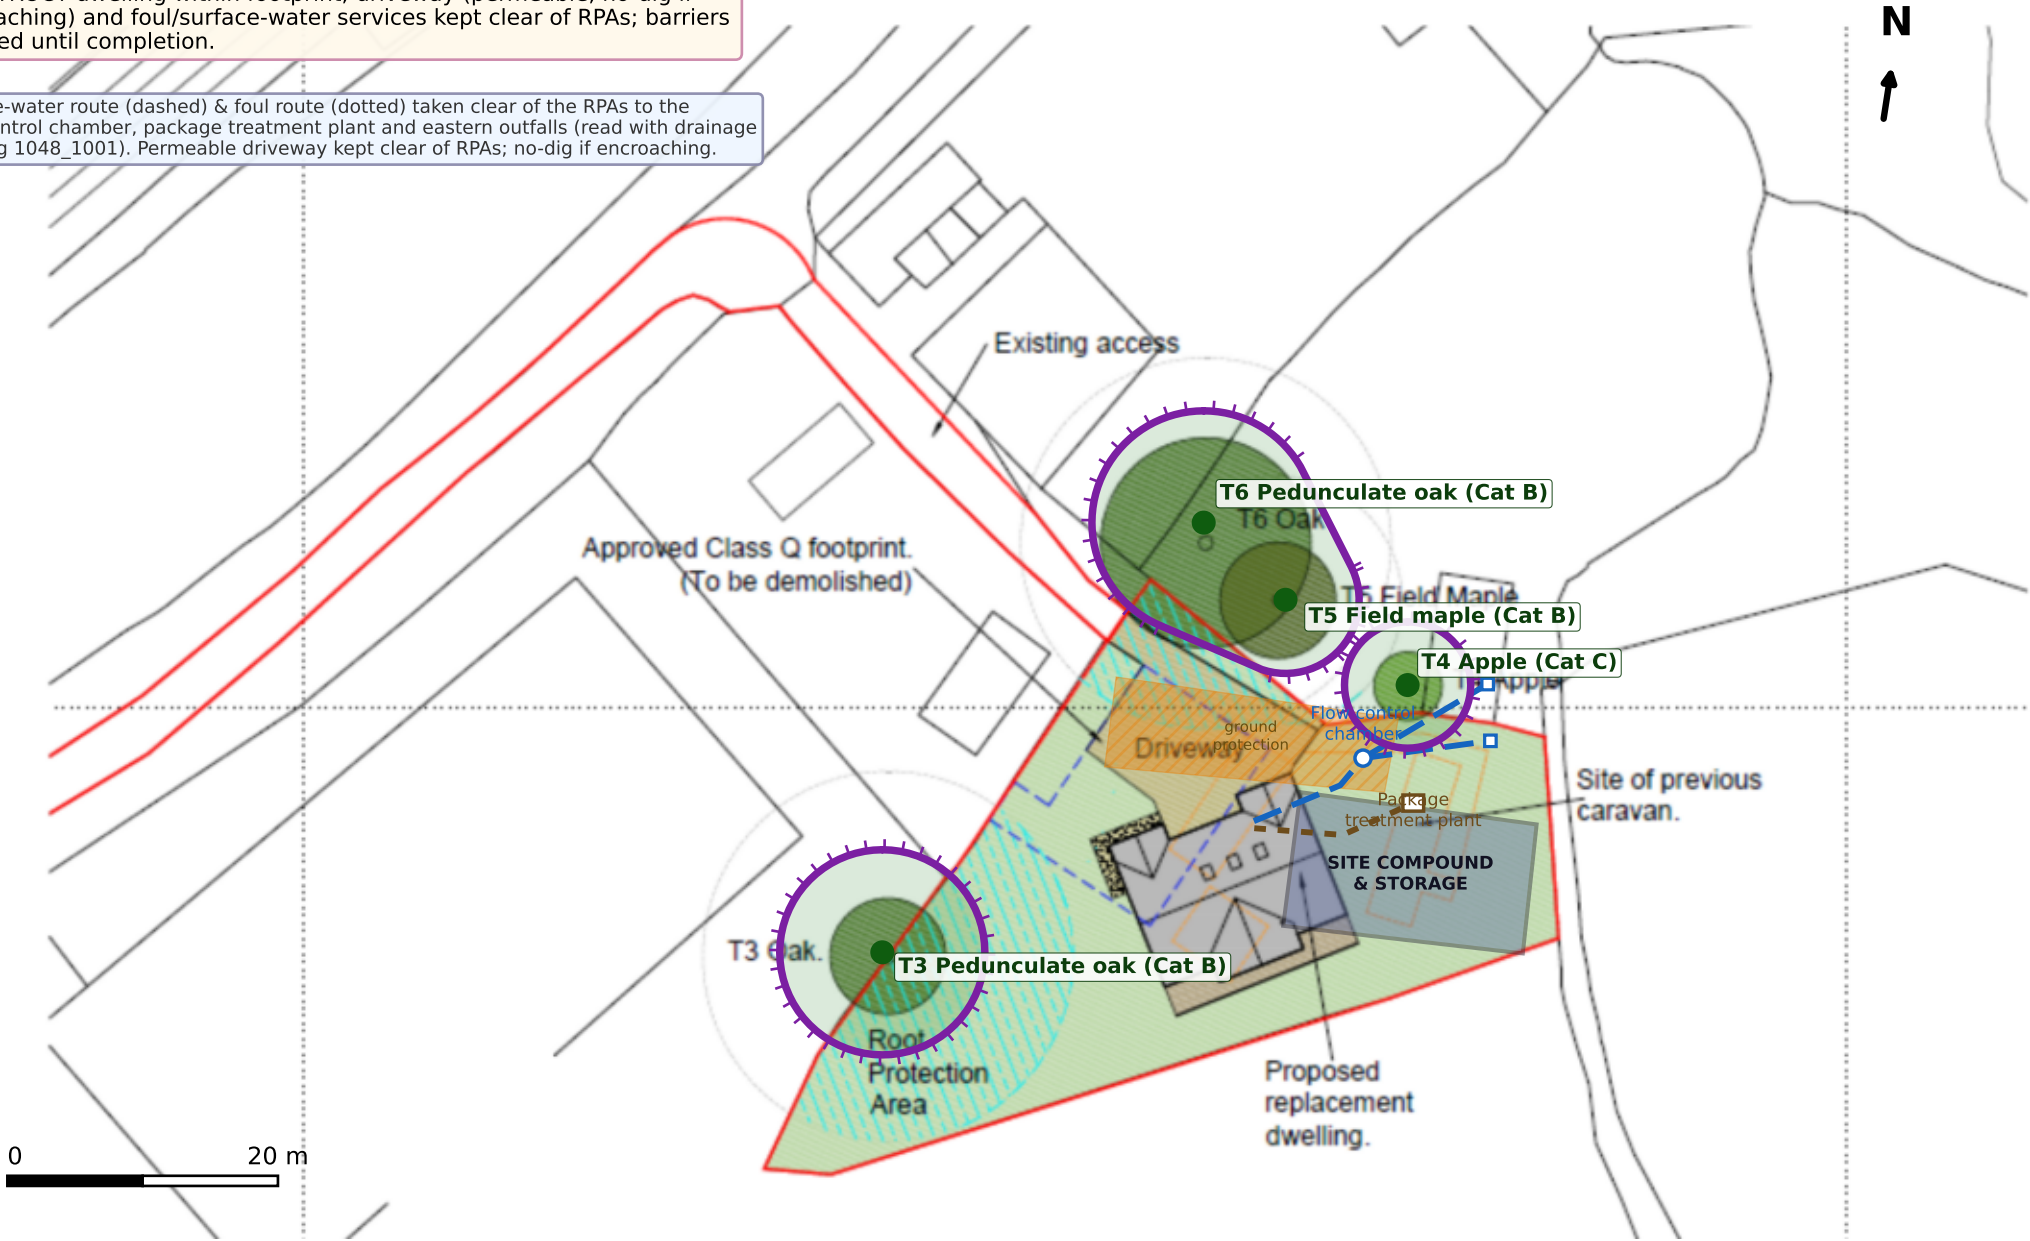

DRAWING TITLE

TREE PROTECTION PLAN - PHASE 2
(CONSTRUCTION)

BASE

Architect Proposed Layout Plan (drawing
154_2502 / Fig 4.1), Simon Harvey
Designs

PROJECT

Replacement dwelling, Gorelands Farm

CLIENT

Mrs Georgina Obbard

PLANNING REF

DC/26/0597

DRAWING No

GF-TTP-004 Rev D

SCALE

Scale bar to govern (A3)

DATE

21 August 2026

PREPARED BY

Alfie Allingham BSc (Hons), FdSc, PTI

LEGEND

- Root Protection Area (= fenced RPZ area)
- RPZ / protective fencing at RPA boundary (BS5837)
- Ground protection within RPA
- Site compound & storage (outside RPAs)
- Tree retained
- Surface-water route
- Foul route

NOTES

- Trees plotted to the architect Proposed Layout Plan
154_2502 Rev A so the RPZ fencing sits around each tree;
RPA radii from the Nov 2025 survey (12 x stem dia., BS5837);
fence set at the RPA or crown edge, whichever is greater.
- Fencing = combined RPA envelope (BS5837 Fig.2); ground
protection where an RPA overlies retained hard standing
(AMS 11.4 / GF-TTP-002).
- Site compound, welfare, parking, material & spoil storage,
plant, wheel-wash & concrete wash-out located outside ALL
RPAs & CEZs (AMS 11.7). 4. No excavation, storage, spoil or
plant within any RPA; all drainage/services routed clear
of RPAs (AMS 11.10). 5. Works within RPAs under arb. supervision.
