

Tree Protection Areas - Construction Exclusion Zones

INSTALLING PROTECTION Protective barriers & 'no-dig' areas of hard standing as shown must be installed before any materials or machinery are brought onto the site and before the commencement of any demolition, general site clearance, ground or construction works of any description.



RETENTION OF PROTECTION All protective measures must remain fully intact, vertical (in the case of barriers), in their approved locations, from the outset of the development and maintained, at all times, until all works have been completed on site, including any earthworks and associated soft landscaping works. Any approved phasing of protective measures must be fully observed and complied with.

RESTRICTIONS Tree Protection Areas/Construction Exclusion Zones are to remain completely undisturbed for the duration of **all** development works. **No** construction activity of any description including but not limited to the following must occur within these areas at any time.

- No excavation of any description.
- No storage, disposal of soil, rubble or materials of any other description.
- No alterations to existing levels or ground conditions.
- No vehicular access, parking or use of any tracked or wheeled machinery of any description.
- No tree works, without the written consent of the Council's Tree Service.
- No erection of temporary structures of any description.
- No storage disposal handling or use of any Chemicals including cement washings.
- No fixtures or fittings of any description, security lighting, signage etc shall be attached to any part of a tree.
- No fires shall be light within 10 metres of the canopies of any tree or spread of any hedge.
- No chemicals, fuel, liquids/waste residues of any other description to be stored or disposed of within close proximity to or drained towards/into protection areas.

PROTECTION AREA SIGNAGE All weather notices as below or similar to be fixed to protective barriers at regular intervals (maximum spacing 5m) throughout site and maintained until completion of **all** development works.

PLANNING COMPLIANCE - The protective measures detailed on this drawing are a legal requirement. Failure to protect the trees/hedges in full accordance with the approved scheme may lead to enforcement action being taken by the Local Authority.

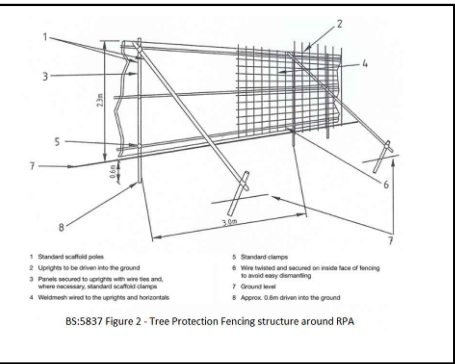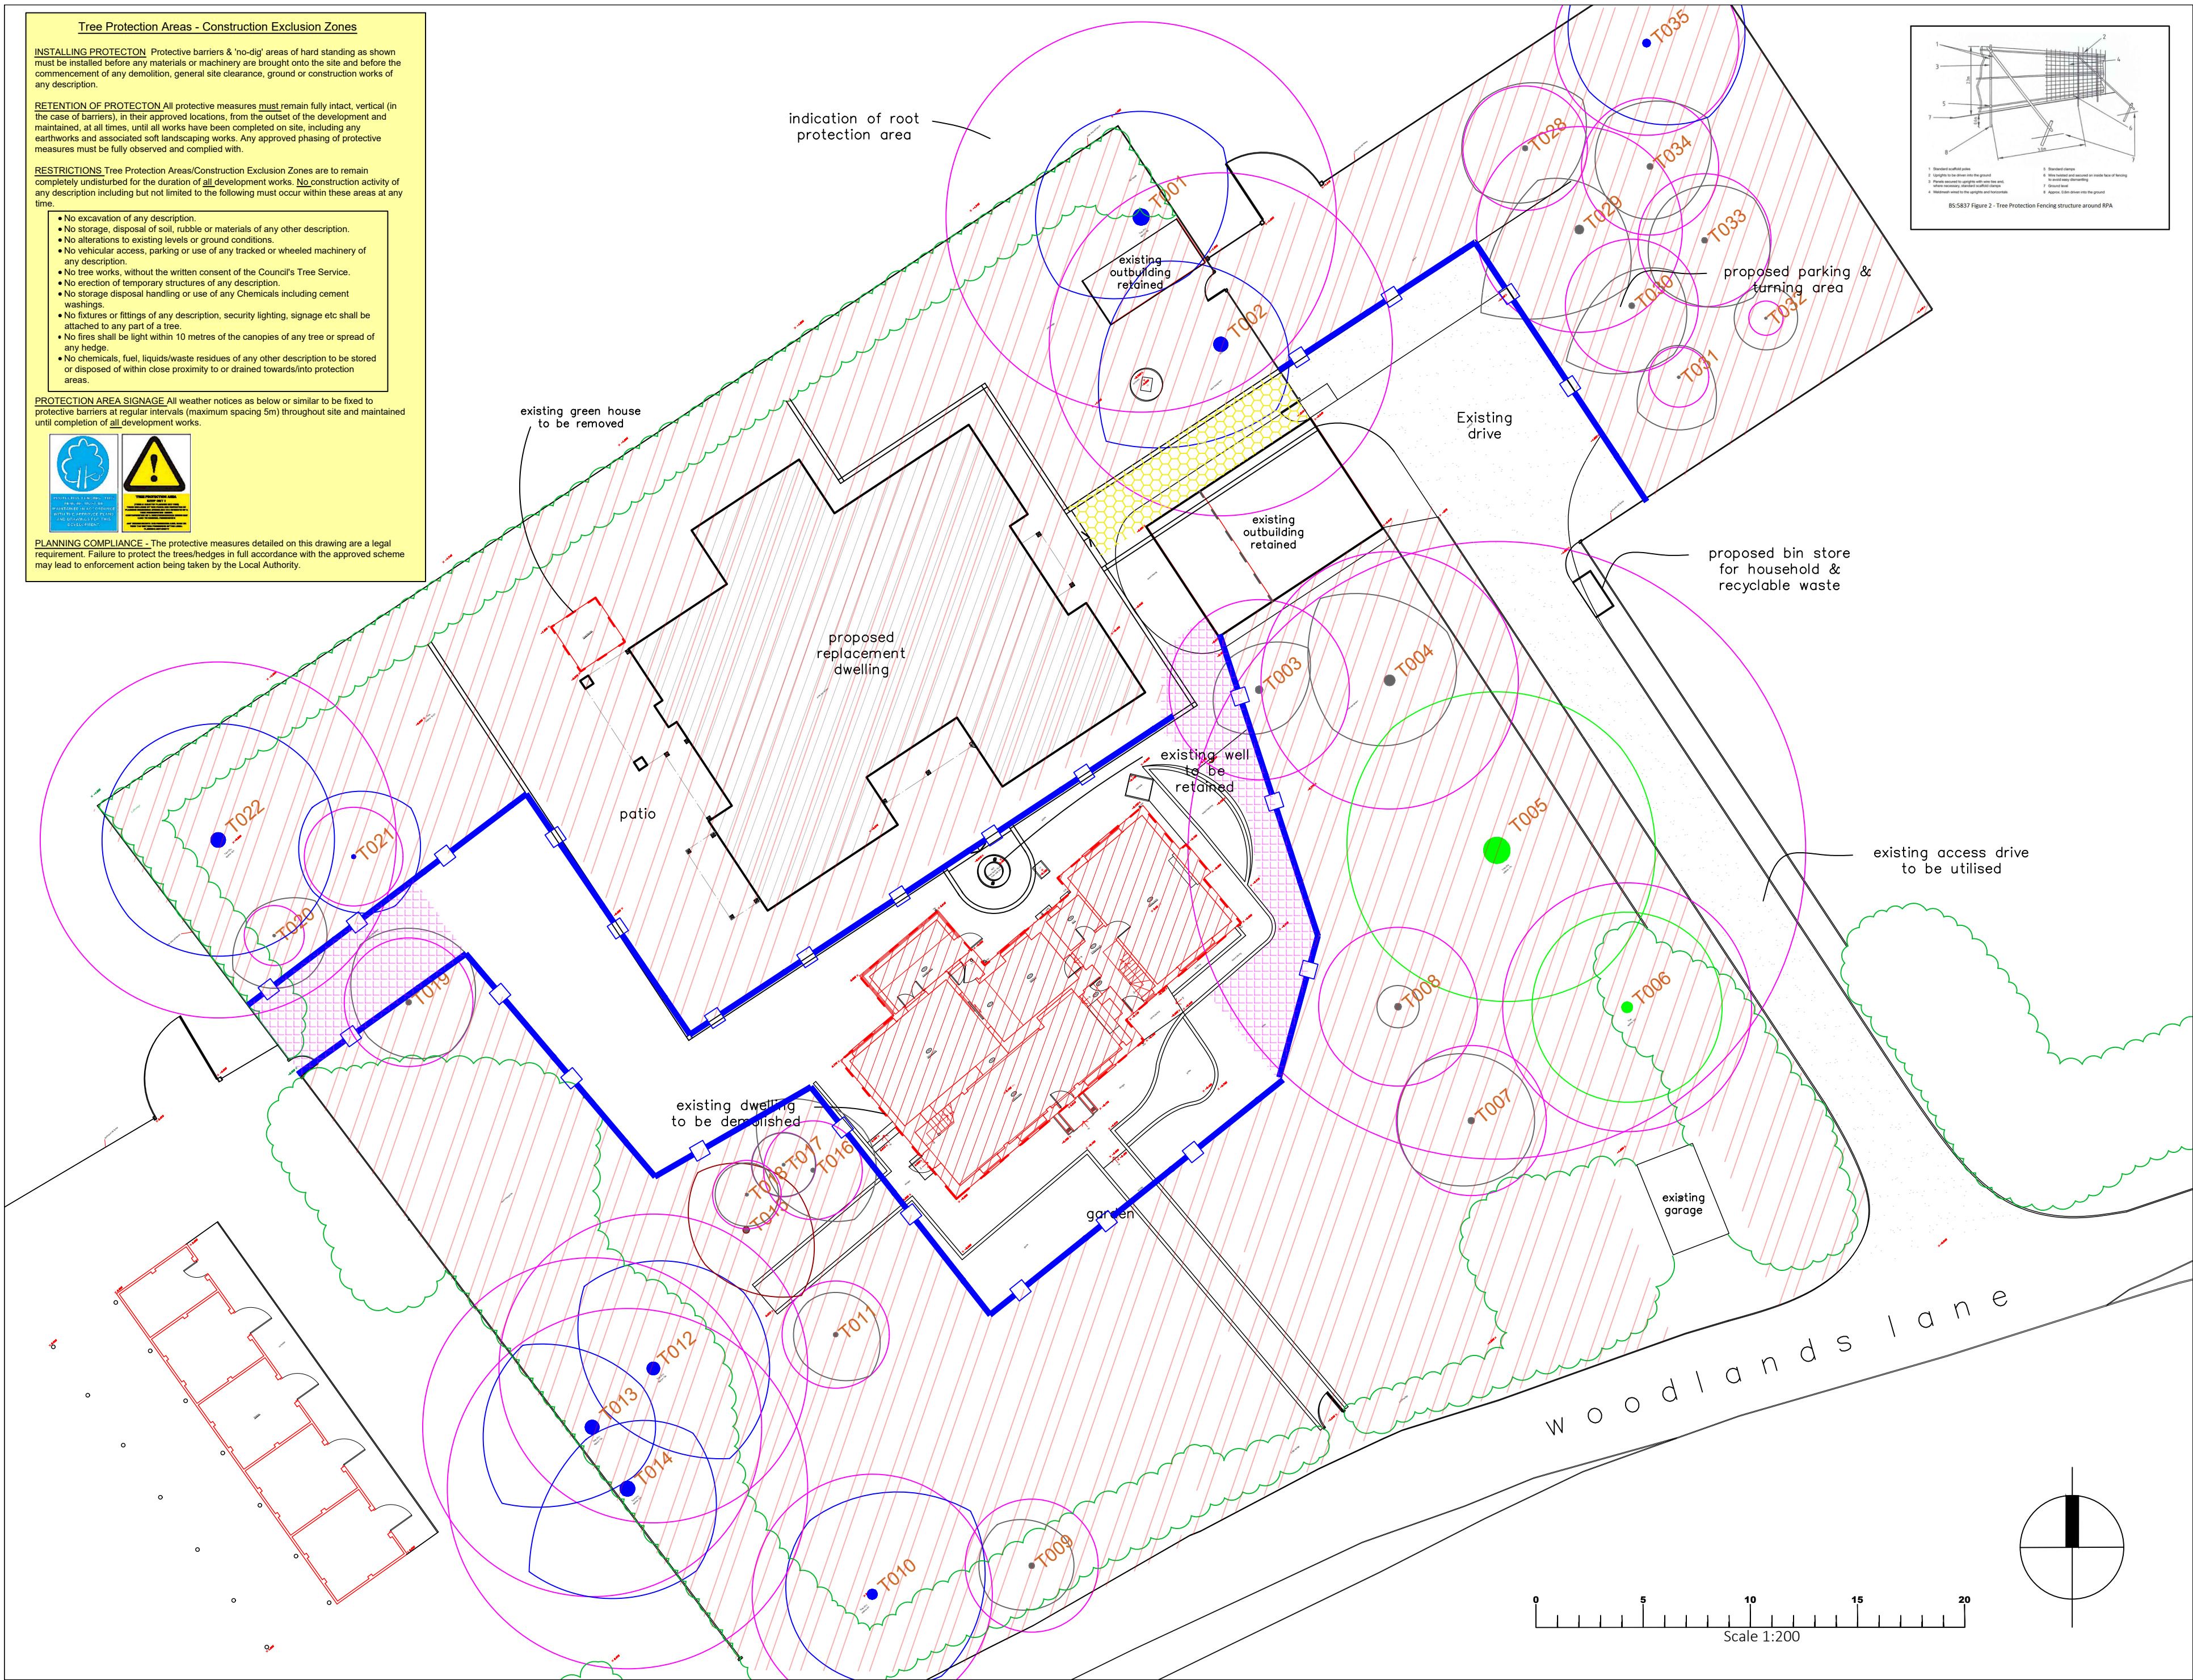

KEY - TREES

T001

HIGH-GRADE CATEGORY 'A' TREE

T002

MEDIUM-GRADE CATEGORY 'B' TREE

T003

LOW-GRADE CATEGORY 'C' TREE

T004

CATEGORY 'U' POOR QUALITY TREE - POTENTIALLY HAZARDOUS

ROOT PROTECTION AREA (RPA)

TEMPORARY TREE PROTECTION FENCING

CONSTRUCTION EXCLUSION ZONE - KEEP OUT!

NO-DIG PATHWAY

EXISTING BUILDING TO BE REMOVED

TEMPORARY GROUND PROTECTION DURING DEMOLITION

BS:5837 TREE PROTECTION PLAN

PHASE 2 - DEMOLITION

Client:
AIMEE & NICK WARNER

Site:
PINWOOD
Colgate
Horsham
West Sussex
RH13 6HU

The position of trees has been taken from a topographical survey provided by the client. The location of smaller trees not included on the topo have been plotted by eye by the tree surveyor.

The position of these trees should not be taken as exact but this plan is considered to be a good representation of tree locations in relation to the property and future building works.

Survey by Sarah Duckworth
Arboricultural Consultant

sarahduckworth@hotmail.com
T:07810440546

Scale 1:200 @ A2
Date: JANUARY 2026 (UPDATED JULY 2026)

Ref:
PINWOOD TPP 06938 2026 PHASE 2 DEMOLITION 0.3

