



ARBORICULTURAL IMPACT ASSESSMENT, METHOD STATEMENT AND TREE PROTECTION PLAN

**Knowe Top Farm
Broadford Bridge
West Chiltington
West Sussex**

Document date: 25th June 2026

Document ref: PJC/7212/26-02 Rev -

This report has been prepared by
PJC Consultancy Ltd
on behalf of
ECE Planning

Document author


Nick Betts HND For M.Arbor.A

Nick has attained an HND in forestry management and is a professional member of the Arboricultural Association. He has worked in the arboricultural and forestry industries for 26 years. He started his career as a forestry worker before qualifying as a tree surgeon, working in both the private and commercial sectors. He has been a practising consultant since 2004. He is a LANTRA accredited professional tree inspector.

Checked by

Peter Davies FdSc Arboriculture M.Arbor.A

Peter has a Foundation Degree in Arboriculture from the University of Brighton and is a professional member of the Arboricultural Association. He has over 15 years' experience in the arboricultural industry, originally working as a groundsman and feller, and progressing into consultancy. He is a LANTRA accredited professional tree inspector.



arboriculture . ecology . landscape



CONTENTS

EXECUTIVE SUMMARY	4
1 INTRODUCTION	5
1.1 Instruction	5
1.2 Objectives of report.....	5
1.3 Contents of report	5
1.4 Documents and information provided.....	5
1.5 Limitations of report	5
2 ARBORICULTURAL IMPACT ASSESSMENT	6
2.1 Site visit.....	6
2.2 The proposals	6
2.3 Tree removals	6
2.4 Access facilitation pruning.....	6
2.5 Levels	6
2.6 Building footings in proximity to trees.....	6
2.7 Services.....	6
2.8 Post development tree pressures and management	7
2.9 Conclusions	7
3 ARBORICULTURAL METHOD STATEMENT.....	8
3.1 General requirements	8
3.2 Phasing of works	8
3.3 Initial tree works.....	8
3.4 Tree protection barriers.....	9
3.5 Storage and handling of harmful chemicals.....	9
3.6 Contractor facilities.....	10
3.7 Services.....	10
3.8 Process if an unforeseen issue relating to trees arises.....	10
Appendix 1: Tree Constraints Plan	11
Appendix 2: Tree Survey Schedule	12
Appendix 3: Tree Retention Plan	13
Appendix 4: Tree Protection Plan.....	14
Appendix 5: Tree Protection Fencing Specification	15
Appendix 6: Example Protective Fencing Sign	16



EXECUTIVE SUMMARY

PJC Consultancy has been instructed by ECE Planning to provide an arboricultural impact assessment and arboricultural method statement to support a full planning application at Knowe Top Farm, Broadford Bridge Road, West Chiltington, for a new building and access road associated with the production of wine.

This report complies with the recommendations of British Standard BS5837: 2012 Trees in relation to design, demolition and construction – Recommendations.

The survey was carried out on 11th June 2026. The tree constraints plan and tree survey schedule can be found at Appendix 1 and Appendix 2 respectively.

The proposed layout has been overlaid with the tree constraints plan in order to identify the impacts to the trees to inform this impact assessment and this information has formed the basis of the tree retention plan at Appendix 3, and the tree protection plan at Appendix 4.

No trees are proposed to be removed; however a small section of hedge will be removed to allow the construction of the new access road.

Subject to the generic and specific tree protection measures recommended within the arboricultural method statement at section 3 of this report being adhered to, I consider that the proposals represent a minor impact on the amenity of the locality in so far as it is contributed to by trees.



1 INTRODUCTION

1.1 Instruction

- 1.1.1 PJC Consultancy has been instructed by ECE Planning to provide an arboricultural impact assessment and arboricultural method statement to support a full planning application at Knowe Top Farm, Broadford Bridge Road, West Chiltington, for a new building and access road associated with the production of wine.
- 1.1.2 This report complies with the recommendations of British Standard BS5837: 2012 Trees in relation to design, demolition and construction – Recommendations (the British Standard).

1.2 Objectives of report

- 1.2.1 This report has been undertaken with the following objectives:
- To identify the tree removals and pruning works that will be required as a result of the proposed development and to assess the impact of the tree works.
 - To assess the potential impact the proposed construction works will have on retained trees and provide recommendations for mitigation measures to reduce the impact on the trees.
 - To provide a protection methodology for retained trees throughout the demolition and construction period, including the above ground and below ground parts of the trees as well as their rooting medium.

1.3 Contents of report

- 1.3.1 This report includes:
- A tree constraints plan and tree survey schedule at Appendices 1 & 2 respectively.
 - An arboricultural impact assessment at section 2, a tree retention plan at Appendix 3.
 - An arboricultural method statement at section 3 and a tree protection plan at Appendix 4.

1.4 Documents and information provided

- 1.4.1 The following documents were used to aid the preparation of this report:
- PJC Initial Arboricultural Report Ref: 5693/21-01
 - Coastline Architecture Drg. No.3002

1.5 Limitations of report

- 1.5.1 The following arboricultural impact assessment and method statement have been prepared for the proposal stated in section 1.1 and using the plans and information listed in section 1.4. The report should not be relied upon if the stated proposal or proposed design changes unless the author confirms the changes do not have a bearing on the arboricultural impacts or recommended mitigation measures.



2 ARBORICULTURAL IMPACT ASSESSMENT

2.1 Site visit

- 2.1.1 The survey was carried out on 11th June 2026. The tree constraints plan and tree survey schedule can be found at Appendix 1 and Appendix 2 respectively.

2.2 The proposals

- 2.2.1 The proposed layout has been overlaid with the tree constraints plan in order to identify the impacts to the trees to inform this impact assessment and this information has formed the basis of the tree retention plan at Appendix 3, and the tree protection plan at Appendix 4.

2.3 Tree removals

- 2.3.1 No trees are proposed to be removed; however, a small section of hedge will be removed to allow the construction of the new access road.

2.4 Access facilitation pruning

- 2.4.1 Based on the information currently available, it is anticipated that the crowns of all remaining retained trees will be located a sufficient distance from proposed construction activities and expected construction access routes so as not to require pruning.
- 2.4.2 Any additional requirements for pruning that cannot be predicted at this stage in the design process (e.g. for contractor compound or movement of large or specialist plant machinery) shall be discussed at the pre-commencement meeting with the project arboriculturist and agreed with the local authority arboricultural officer.

2.5 Levels

- 2.5.1 The levels of the site are broadly flat and level. The existing levels have been incorporated into the design process and no change of levels are proposed.

2.6 Building footings in proximity to trees

- 2.6.1 All proposed buildings will be located outside the root protection areas of retained trees, therefore use of specialist foundations for root protection is not deemed necessary.
- 2.6.2 NHBC guidelines on foundation depth in proximity to trees should be followed. This will be determined by a structural engineer and should be guided by information in this report as well as appropriate sampling to determine soil profiles at the site.

2.7 Services

- 2.7.1 Details of the routing of services for the proposed development are not currently available. All underground services should be located outside the root protection areas of retained trees and above ground services should be located outside the anticipated mature crown spreads. Sympathetic methodology to enable the installation of services within root protection areas (in certain instances) is available, however there will always be a potential arboricultural impact and arboricultural advice must be sought regarding the suitability of these methods before they are relied upon. If it is achievable, root protection areas should always be completely avoided.
- 2.7.2 Once details of the routing of new services become available, prior to commencement, these shall be reviewed by the project arboriculturist. The arboriculturist shall then confirm either that no works will be carried out within root protection areas or provide details of the methodology required to ensure the works are carried out in accordance with NJUG4



‘Guidelines for the planning, installation and maintenance of utilities in proximity to trees’ and BS5837: 2012.

2.8 Post development tree pressures and management

- 2.8.1 The proposed building will not be a habitable dwelling and is located at a distance from retained trees so that seasonal nuisance and shading should not be regarded as an issue that would require future pruning.

2.9 Conclusions

- 2.9.1 Trees requiring removal to facilitate the proposed development comprise a short section of category B hedge. All other arboricultural features will be retained and incorporated into the proposed site layout.
- 2.9.2 All proposed buildings and areas of new surfacing will be located outside the root protection areas of retained trees. Provided the exclusion zones and methodologies described in the arboricultural method statement and tree protection plan are followed, trees proposed for retention should not be adversely affected by the construction works.
- 2.9.3 Based on the above assessment, trees recommended for retention in this report can be protected during the construction period and successfully integrated into the site post development.



3 ARBORICULTURAL METHOD STATEMENT

3.1 General requirements

- 3.1.1 The arboricultural method statement and tree protection plan shall remain on site for the duration of construction and be available to site operatives at all times. All operatives at the site shall be briefed about tree related factors as part of their site induction.
- 3.1.2 Any variation from the methodology described in this method statement shall be discussed with the supervising arboriculturist and agreed with the local authority arboricultural officer.

3.2 Phasing of works

- 3.2.1 To ensure trees are protected throughout the development, the proposed development shall occur in the following order:

Table 1: Phasing of works

Works Order	Operation	Notes
1	Initial tree works.	The tree works contractor shall undertake the tree removals specified in the arboricultural impact assessment. Completion of these works will be required to enable the installation of tree protection barriers.
2	Installation of tree protection barriers.	Tree protection fencing shall be installed in the locations shown on the tree protection plan and to the specification described in this method statement.
3	Construction phase.	The tree protection barriers shall be maintained, and the construction exclusion zones observed throughout the construction phase.
4	Soft landscaping phase.	The tree protection barriers shall be dismantled when external construction and hard landscape operations have been completed and plant machinery or excess construction materials have been removed from site.

3.3 Initial tree works

- 3.3.1 The tree removals specified in the arboricultural impact assessment shall be carried out as the first stage of development. Any requirements for access facilitation pruning which have not been anticipated on the date of this report shall be discussed at the pre-commencement meeting with the project arboriculturist and be communicated to the local authority arboricultural officer.
- 3.3.2 Tree stumps and vegetation located within the root protection areas of retained trees shall be cleared with controlled hand tools (e.g. stump grinder/brush cutter). Plant machinery shall not be used to scrape vegetation, 'grub out' stumps within root protection areas, or access the site until the tree protection barriers have been installed.
- 3.3.3 If bonfires are lit to dispose of arisings from the vegetation or tree clearance works, an assessment of wind direction and strength shall be made to ensure flames cannot extend within 5m of any part of a retained tree. No bonfires shall be lit within a root protection area.
- 3.3.4 Trees should be checked for protected species before works are undertaken. It is against the law to disturb bats or their roosts under the Conservation of Habitat and Species Regulations. Nesting birds are protected by the Wildlife and Countryside Act. If protected species are discovered, Natural England should be contacted for advice.



- 3.3.5 The tree works contractors should carry out all tree works to BS3998: 2010 Tree works – recommendations as modified by research that is more recent. They should also carry relevant, adequate and up to date insurance.
- 3.3.6 It is suggested that an Arboricultural Association approved contractor carry out all tree works. Approved contractors are expected to work to industry best standards. The Arboricultural Association website (www.trees.org.uk) contains contact details and information on engaging a suitable contractor.

3.4 Tree protection barriers

- 3.4.1 The root protection areas of retained trees must be left free from disturbance, and protected from contamination or compaction during the proposed works.
- 3.4.2 The tree protection fencing shall be installed before any plant activity, ground works or construction activities commence at the site. They shall be maintained in situ until the soft landscaping phase of development when all other construction activities in the vicinity have been completed, and excess construction materials and plant machinery have been removed from site. Any damage that occurs to the tree protection barriers during the construction period must be rectified immediately, prior to other construction activities recommencing in the vicinity.
- 3.4.3 Tree protection fencing shall be installed in the locations shown on the tree protection plan. The specification for tree protection fencing shall be metal welded mesh panels (e.g. Heras panels), in concrete or rubber feet. The panels shall be supported by metal stabiliser struts mounted on either a base plate secured by ground pins, or in a block tray (refer to Appendix 2). Any variation from this specification for tree protection fencing shall be discussed with the project arboriculturist and agreed in writing with the local authority arboricultural officer.
- 3.4.4 Signs shall be affixed to the fencing as shown in Appendix 3 to explain its purpose. The signs shall be affixed at a reasonable size and frequency to ensure they are easily visible to operatives at the site.
- 3.4.5 The areas protected by tree protection fencing shall be referred to as the construction exclusion zones. The following restrictions shall apply within the construction exclusion zones:
- No vehicular access shall be permitted unless on adequate temporary ground protection measures that have been agreed with the project arboriculturist.
 - Regular pedestrian access shall be restricted unless on suitable ground protection measures agreed with the project arboriculturist.
 - No storage of construction materials shall occur.
 - No storage of building spoil or construction debris (including short-term temporary stockpiling) shall occur.
 - No harmful chemicals shall be stored or handled.
 - No fires shall be permitted.
 - No mechanical excavation including regrading of levels shall occur.
 - There shall be no change in ground level unless undertaken under the supervision of the project arboriculturist.
 - No construction activities including installation of new permanent hard standing shall be undertaken unless otherwise specified in this method statement.

3.5 Storage and handling of harmful chemicals

- 3.5.1 Provision must be taken to prevent the storage and handling of harmful chemicals within the root protection areas of retained trees. Harmful chemicals include fuels, oils, bitumen,



builder's sand (which has a high salt content) and cement. Provision shall also be made to prevent the storage and handling

- 3.5.2 adequate, bunded ground protection measures are implemented to prevent of harmful chemicals in areas proposed for further planting if the existing soil is intended to be retained.
- 3.5.3 Cement mixing shall always occur outside the construction exclusion zones. If cement mixing is to occur close to the construction exclusion zones, or there is the potential for cement washings to leech into a root protection area, adequate, bunded ground protection measures must be used. This could comprise impermeable plastic sheeting under wooden boards (to prevent tears) surrounded by a raised lip.
- 3.5.4 All other chemicals that are harmful to trees must be stowed in suitable containers and stored away from the construction exclusion zones unless spillages leeching into root protection areas.

3.6 Contractor facilities

- 3.6.1 A suitable location for site cabins, contractor parking and site facilities for operatives shall be agreed with the project arboriculturist. These facilities must be located outside the root protection areas of all retained trees unless on adequate ground protection measures that have been signed off with the project arboriculturist (potentially including existing hard standing). Provision must be taken to prevent exhaust fumes or hot air from generators or kitchen facilities from damaging foliage within the crowns of retained trees.

3.7 Services


- 3.7.1 The routing of new services for the development is not available on the date of this report. These must be signed off by the project arboriculturist before implementation. Wherever possible, the services must completely avoid the root protection areas of retained trees. Where this is not feasible, the arboriculturist shall provide an arboricultural method statement (to be signed off by the local authority arboricultural officer before implementation) detailing any sympathetic methodologies that are required to minimise damage to tree roots (as described in NJUG4 'Guidelines for the planning, installation and maintenance of utilities in proximity to trees' and BS5837: 2012).

3.8 Process if an unforeseen issue relating to trees arises

- 3.8.1 If significant root growth is disturbed during construction activities that are not within the scope of this report, the work shall cease until the project arboriculturist has been consulted. Roots greater than 25mm in diameter or dense/matted fibrous roots shall be considered significant root growth. It should be remembered that whilst root protection areas are part of industry best practice, tree root growth is influenced by a number of factors and may not conform to expected ideals.
- 3.8.2 If at any time during the construction process, damage is inadvertently caused to a tree, the project arboriculturist shall be notified to assess the likely implications and to prescribe potential remedial measures to be implemented. Damage can be in the form of chemical or fuel spillage, mechanical damage to either the above ground parts of the tree or the roots, fire or any other unforeseen circumstance.



Appendix 1: Tree Constraints Plan

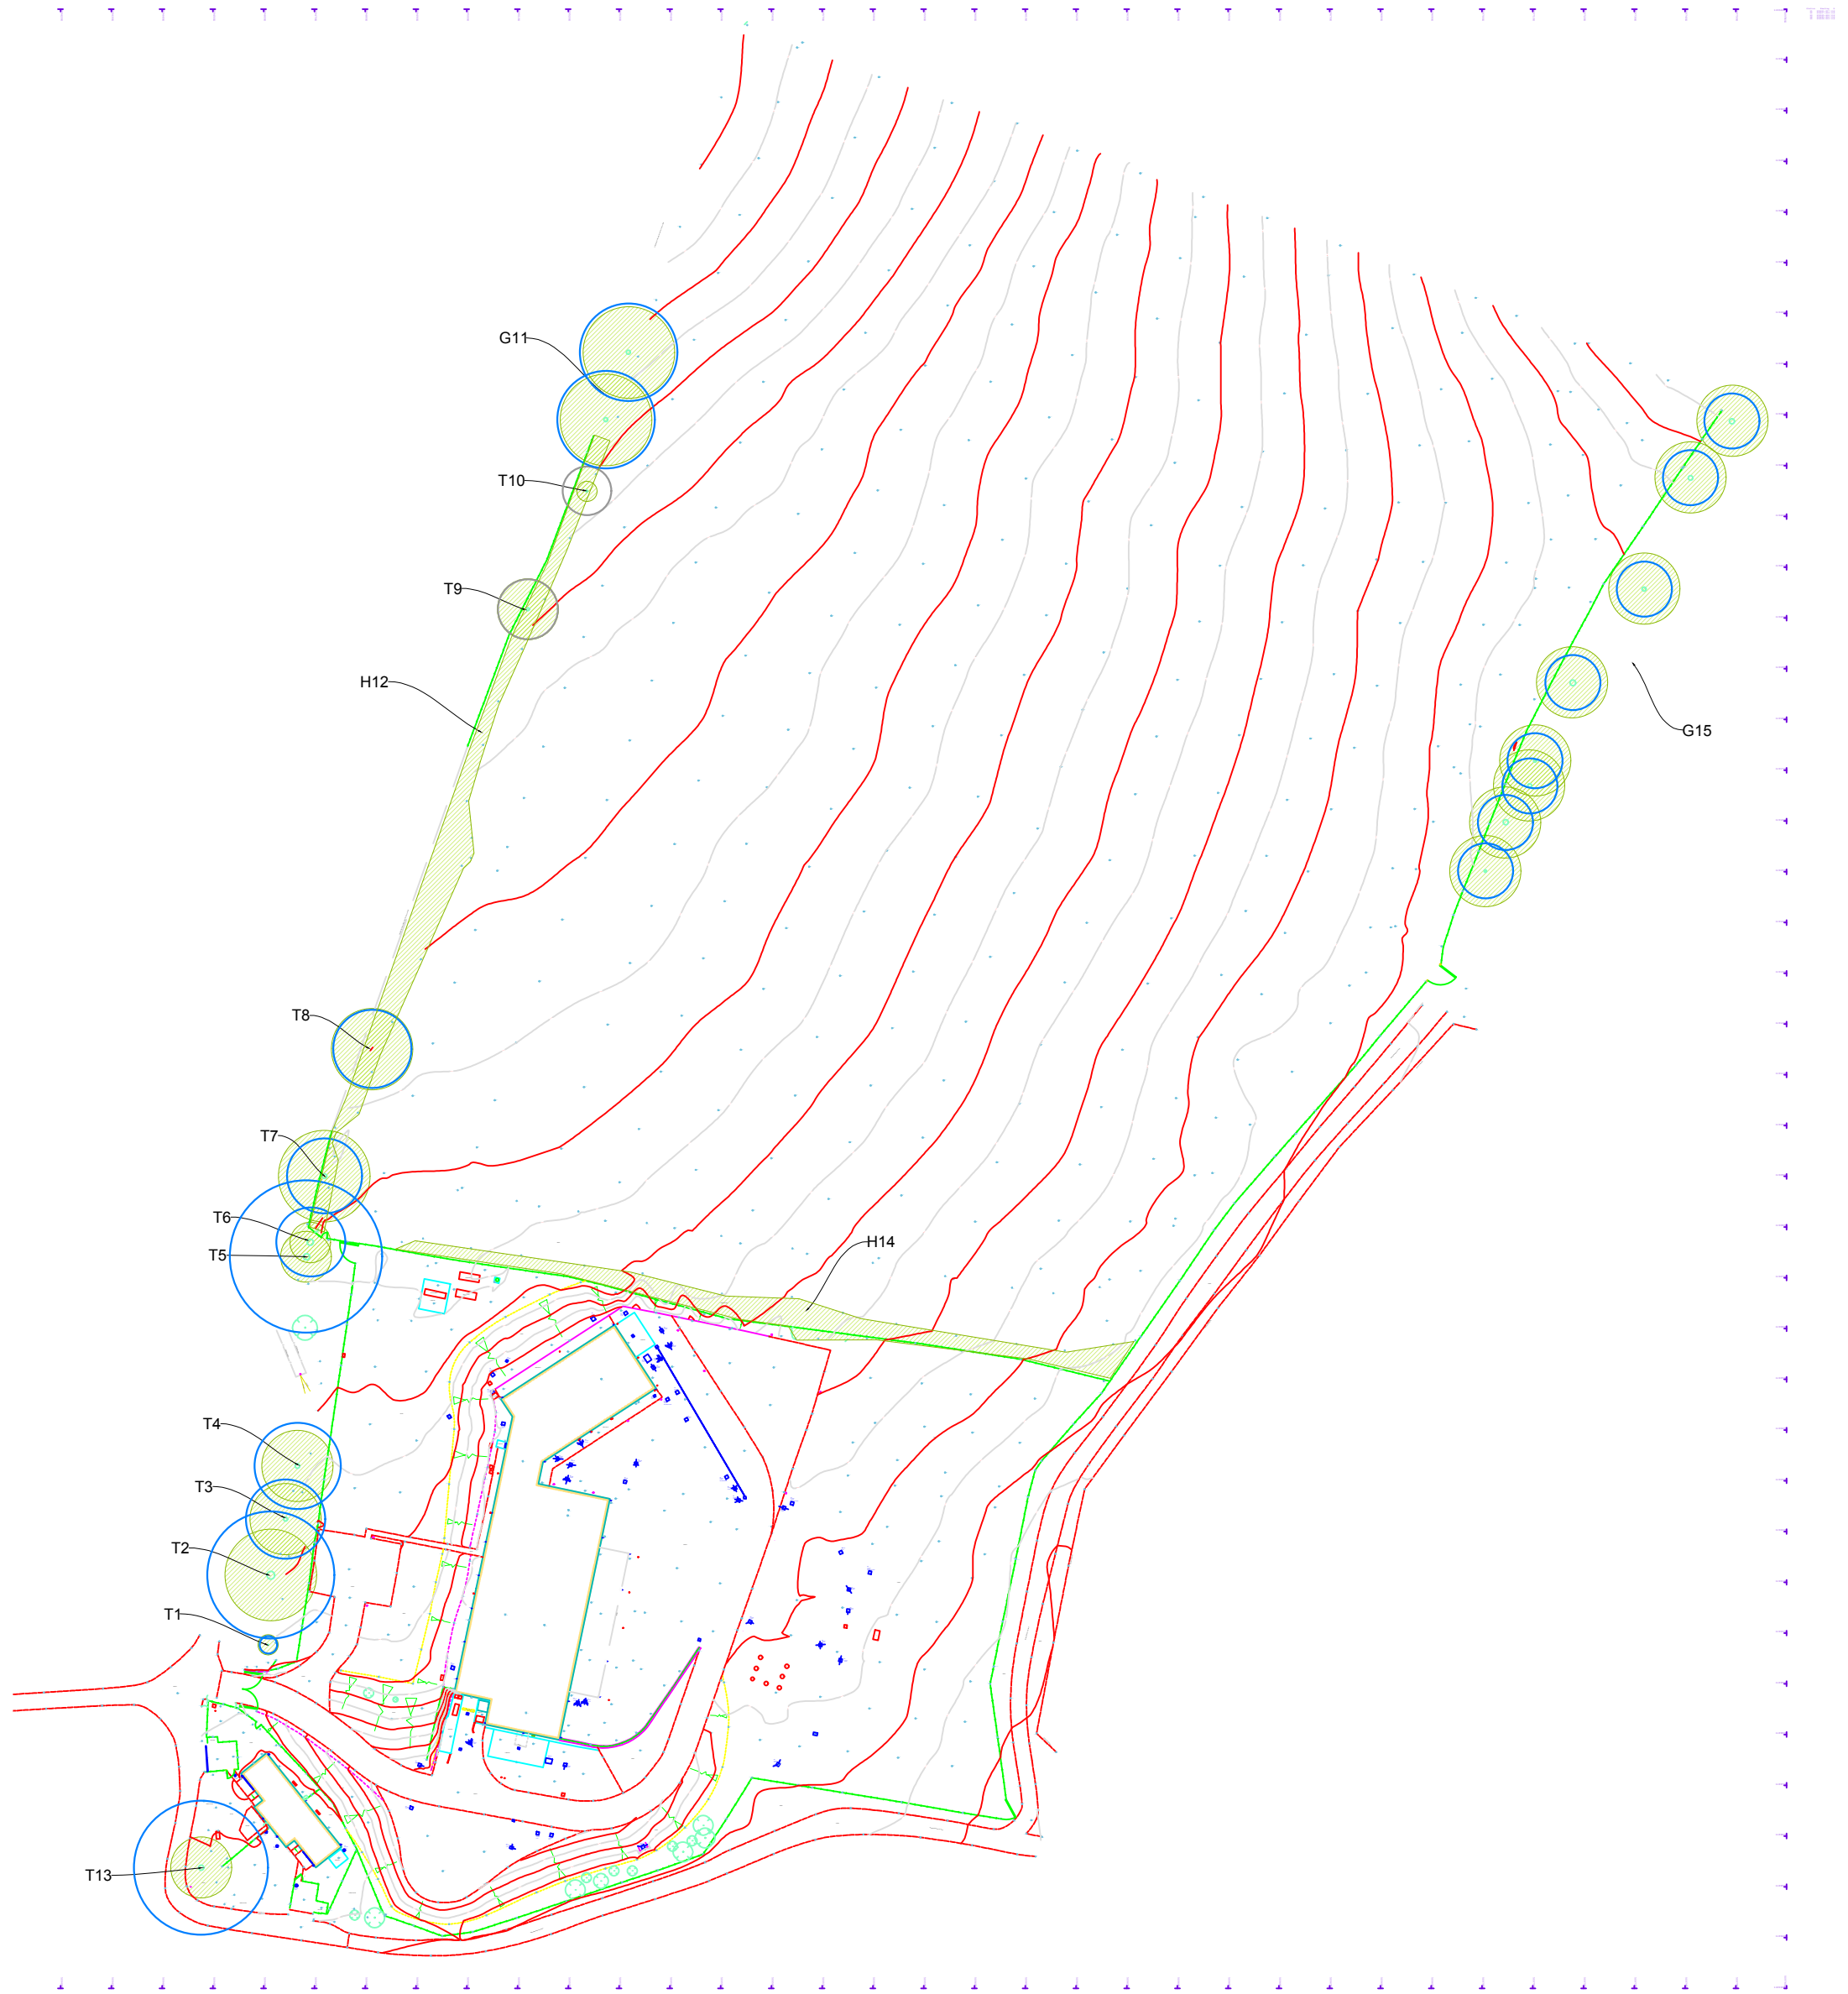

* Tree categorised in accordance with BS 5837:2012 'Trees in relation to design, demolition and construction - Recommendations'.


Tree survey schedule contains further information for each tree.

This drawing should be viewed in colour.

Tree numbers suffixed with PA indicate the tree position is approximate.

Key:

-  Root protection area for category A* tree
-  Root protection area for category B* tree
-  Root protection area for category C* tree
-  Root protection area for category U* tree
-  Tree canopy



Drawing no: PJC/7212/26/A Rev: - Sheet number: 1 of 1

Client and site:
ECE Planning

Knowe Top Farm
West Chilmington
West Sussex


Drawing title: Tree Constraints Plan

Date drawn: 25/06/2026

Scale: 1:1250 at A3

Drawn by: NB

Checked by: PD



PJC Consultancy
The Watermill, The Mill Business
Park, Maidstone Road, Ashford,
Kent, TN26 1AE.

t: 01233 225365
e: contact@pjconsultancy.com
w: www.pjconsultancy.com



Appendix 2: Tree Survey Schedule

Site: Knowe Top Farm, West Chiltington, W. Sussex

Survey date: 11th June 2026

Surveyor: Nick Betts

Tree Survey Schedule



Tree ref.	Species	Height (m)	Stem diameter (mm)	Branch spread (m)	Crown clearance (m)	Age class	Physiological condition	Structural condition	Comments	Preliminary management recommendation	Category grading	Root Protection Area (m ²)	Root Protection Radius (m)
T1	Ash, (<i>Fraxinus excelsior</i>)	6	141	N: 2 E: 2 S: 2 W: 2	Crown: 2 Branch: 2	Semi mature	Fair	Good	No major visible defects	No action required at date of survey	B1	9.0	1.7
T2	Pedunculate oak, (<i>Quercus robur</i>)	16	1039	N: 9 E: 9 S: 9 W: 9	Crown: 5 Branch: 5	Mature	Good	Good	No major visible defects	No action required at date of survey	B2	488.4	12.5
T3	Pedunculate oak, (<i>Quercus robur</i>)	15	650	N: 7 E: 7 S: 7 W: 7	Crown: 5 Branch: 5	Mature	Good	Good	No major visible defects	No action required at date of survey	B2	191.2	7.8
T4	Pedunculate oak, (<i>Quercus robur</i>)	16	710	N: 7 E: 7 S: 7 W: 7	Crown: 6 Branch: 6	Mature	Good	Good	No major visible defects	No action required at date of survey	B2	228.1	8.5
T5	Pedunculate oak, (<i>Quercus robur</i>)	16	1600	N: 6 E: 6 S: 6 W: 6	Crown: 5 Branch: 5	Mature	Good	Good	No major visible defects	No action required at date of survey	B2	707.0	15.0
T6	Pedunculate oak, (<i>Quercus robur</i>)	16	565	N: 4 E: 4 S: 4 W: 4	Crown: 6 Branch: 6	Mature	Good	Good	No major visible defects	No action required at date of survey	B2	144.4	6.8

Site: Knowe Top Farm, West Chiltington, W. Sussex

Survey date: 11th June 2026

Surveyor: Nick Betts

Tree Survey Schedule



Tree ref.	Species	Height (m)	Stem diameter (mm)	Branch spread (m)	Crown clearance (m)	Age class	Physiological condition	Structural condition	Comments	Preliminary management recommendation	Category grading	Root Protection Area (m ²)	Root Protection Radius (m)
T7	Pedunculate oak, (Quercus robur)	16	620	N: 9 E: 9 S: 9 W: 9	Crown: 6 Branch: 6	Mature	Good	Good	No major visible defects	No action required at date of survey	B2	173.9	7.4
T8	Pedunculate oak, (Quercus robur)	15	640	N: 8 E: 8 S: 8 W: 8	Crown: 5 Branch: 5	Mature	Good	Good	No major visible defects	No action required at date of survey	B2	185.3	7.7
T9	Field maple, (Acer campestre)	9	489	N: 6 E: 6 S: 6 W: 6	Crown: 3 Branch: 3	Mature	Fair	Fair	No major visible defects	No action required at date of survey	C2	108.2	5.9
T10	Field maple, (Acer campestre)	6	400	N: 2 E: 2 S: 2 W: 2	Crown: 3 Branch: 3	Mature	Fair	Fair	No major visible defects	No action required at date of survey	C2	72.4	4.8
G11	Pedunculate oak, (Quercus robur)	18-20	800	N: 9 E: 9 S: 9 W: 9	Crown: 6 Branch: 6	Mature	Good	Good	No major visible defects	No action required at date of survey	B2	289.6	9.6
H12	Hawthorn, (Crataegus monogyna) Blackthorn, (Prunus spinosa)	2-3	200	N: 2 E: 2 S: 2 W: 2	Crown: 0 Branch: 0	Mature	Fair	Fair	No major visible defects	No action required at date of survey	B2	18.1	2.4

Site: Knowe Top Farm, West Chiltington, W. Sussex

Survey date: 11th June 2026

Surveyor: Nick Betts


Tree Survey Schedule



Tree ref.	Species	Height (m)	Stem diameter (mm)	Branch spread (m)	Crown clearance (m)	Age class	Physiological condition	Structural condition	Comments	Preliminary management recommendation	Category grading	Root Protection Area (m ²)	Root Protection Radius (m)
T13	Pedunculate oak, (Quercus robur)	15	1100	N: 6 E: 6 S: 6 W: 6	Crown: 4 Branch: 4	Mature	Good	Good	No major visible defects	No action required at date of survey	B2	547.5	13.2
H14	Hawthorn, (Crataegus monogyna) Blackthorn, (Prunus spinosa)	3-6	200	N: 2 E: 2 S: 2 W: 2	Crown: 0 Branch: 0	Mature	Fair	Fair	No major visible defects	Section to be removed to allow for construction of access road	B2	18.1	2.4
G15	Pedunculate oak, (Quercus robur)	6-18	450	N: 7 E: 7 S: 7 W: 7	Crown: 5 Branch: 5	Mature	Good	Good	No major visible defects	No action required at date of survey	B2	91.6	5.4



Appendix 3: Tree Retention Plan

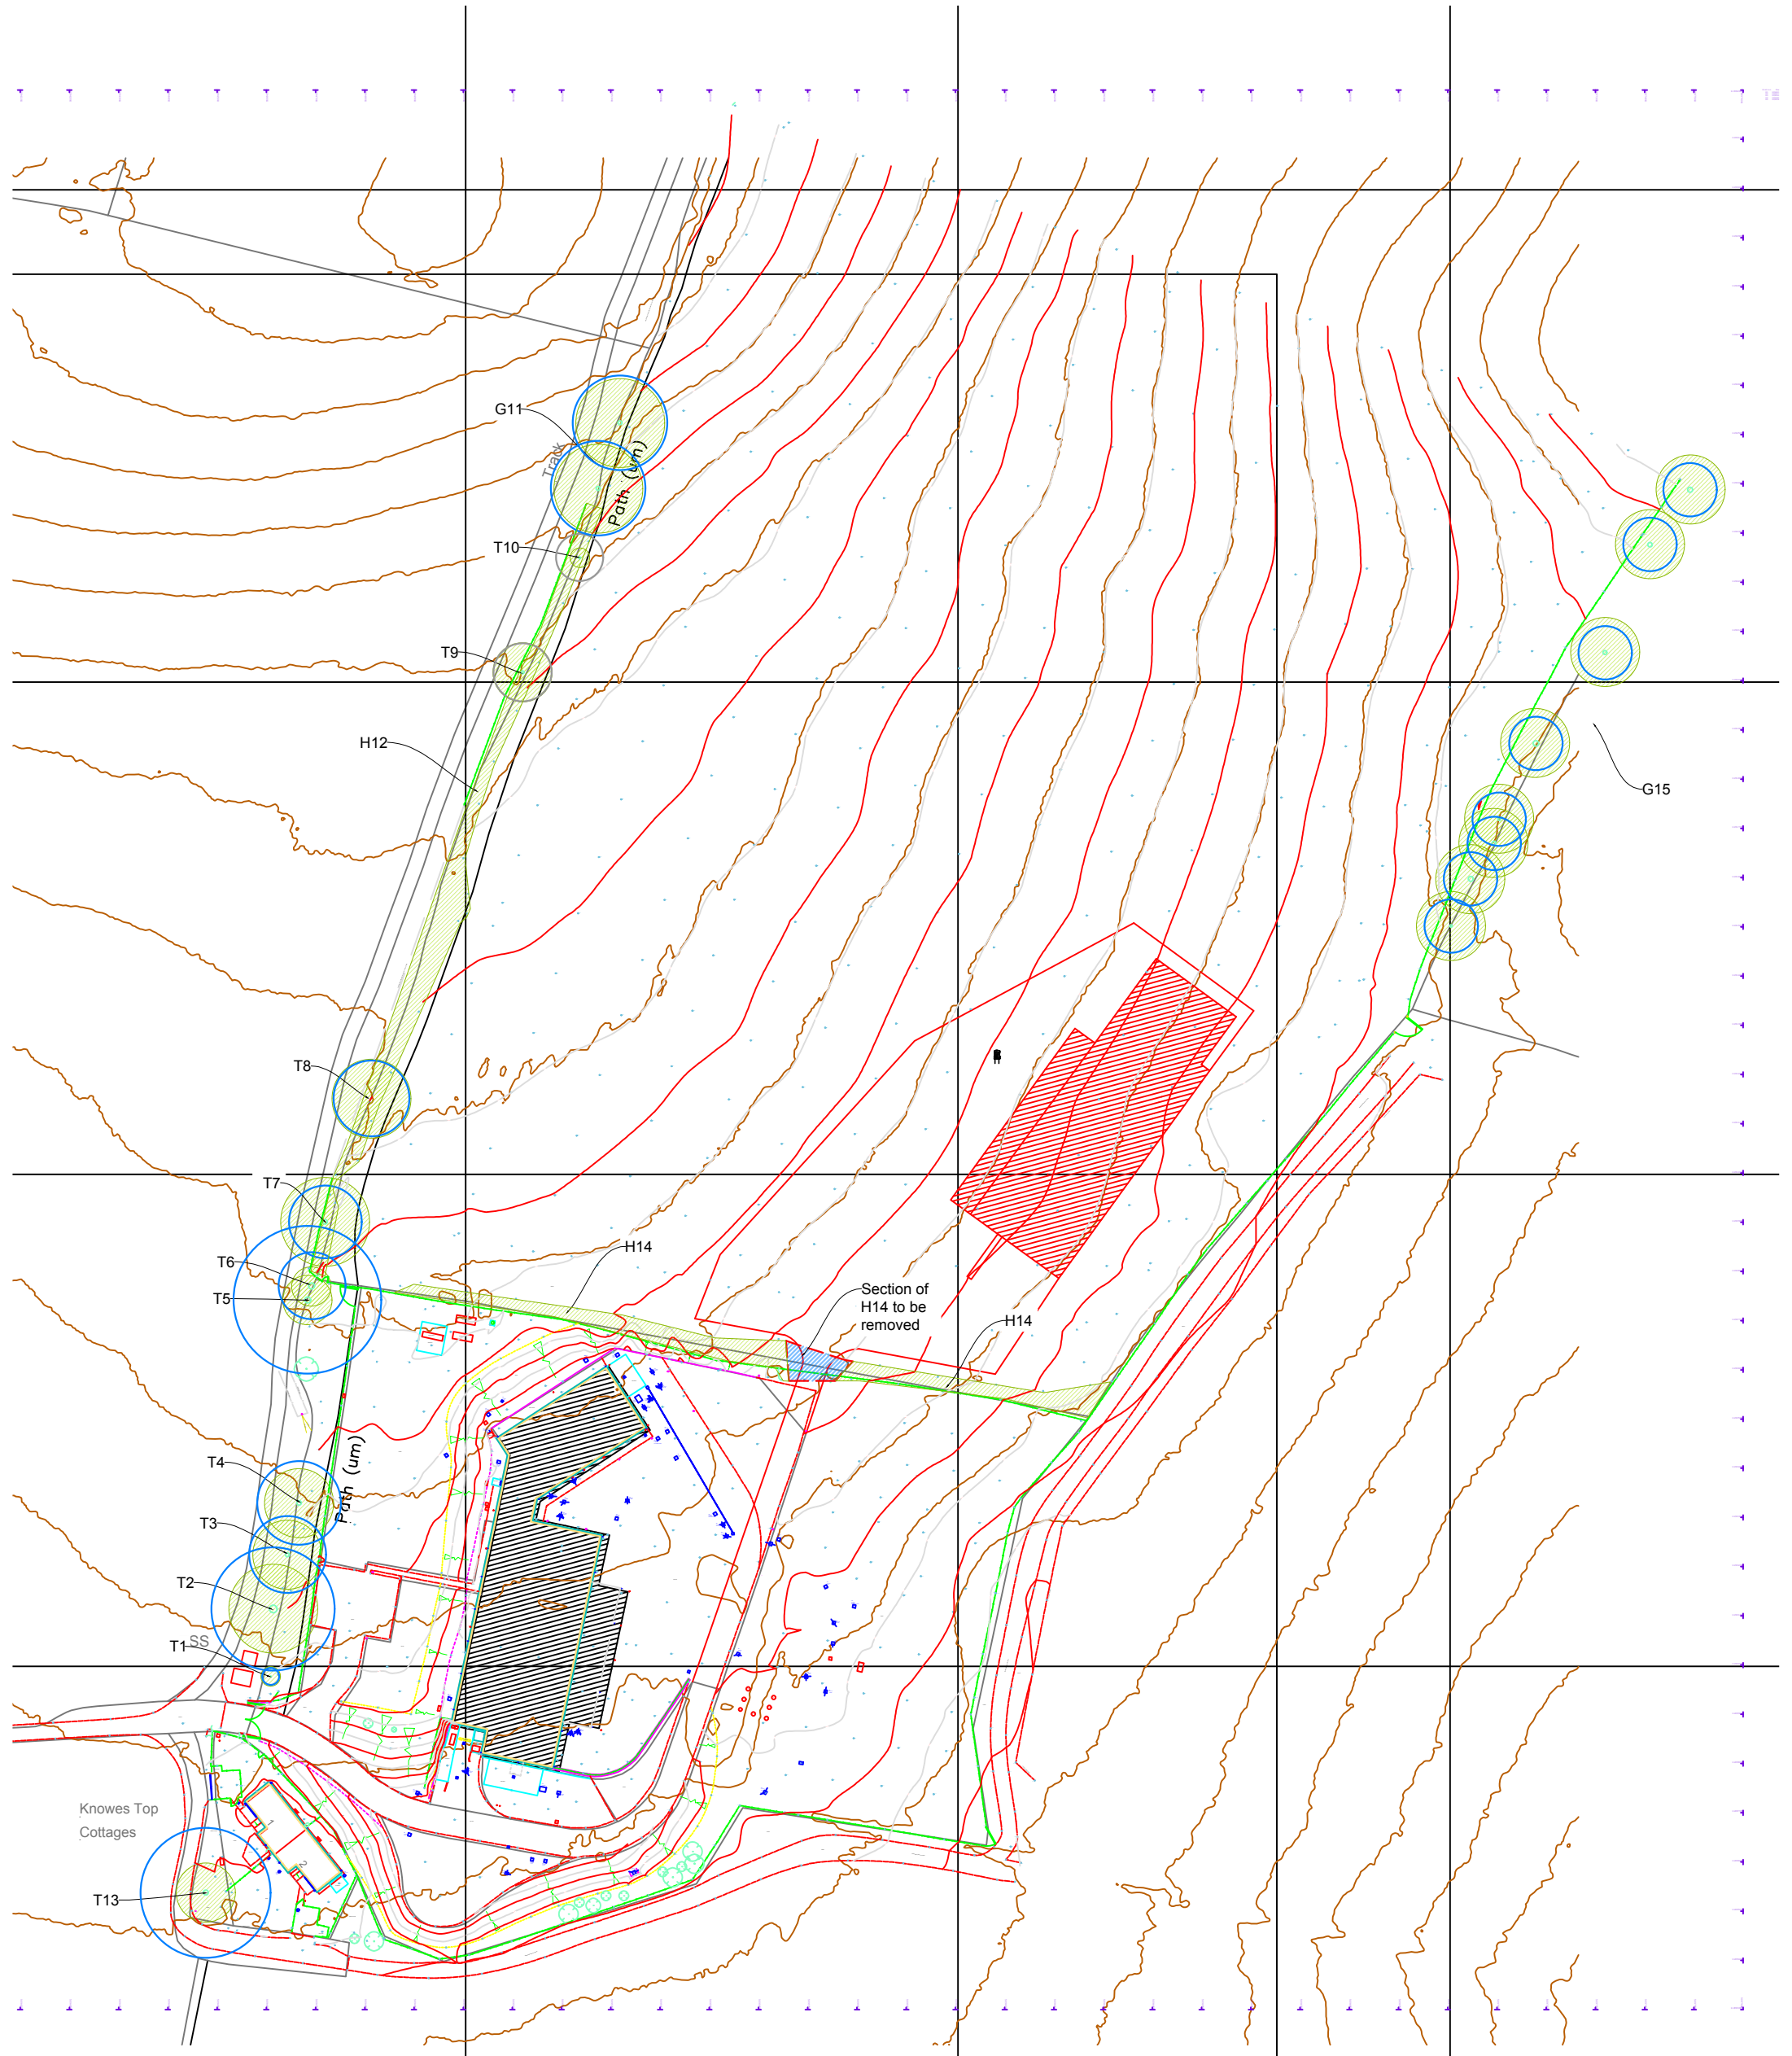

* Tree categorised in accordance with BS 5837:2012 'Trees in relation to design, demolition and construction - Recommendations'.

Tree Survey Schedule contained within the arboricultural report ref. PJC/7212/26-02 contains further information for each tree.

This drawing should be viewed in colour.

Key:

○

Root protection area for category A* tree to be retained

○

Root protection area for category B* tree to be retained

○

Root protection area for category C* tree to be retained

○

Root protection area for category U* tree to be retained

○

Canopy of tree to be retained

○

Canopy of category A* tree to be removed

○

Canopy of category B* tree to be removed

○

Canopy of category C* tree to be removed

○

Canopy of category U* tree to be removed

Drawing no: PJC/7212/26/B

Rev: -

Sheet number: 1 of 1

Client and site:
ECE Planning

Knowe Top Farm
West Chiltington
West Sussex

Drawing title: Tree Retention Plan

Date drawn: 25/06/2026

Scale: 1:1250 at A3

Drawn by: NB


Checked by: PD

PJC Consultancy
The Watermill, The Mill Business Park, Maidstone Road, Ashford, Kent, TN26 1AE.

t: 01233 225365
e: contact@pjconsultancy.com
w: www.pjconsultancy.com



Appendix 4: Tree Protection Plan

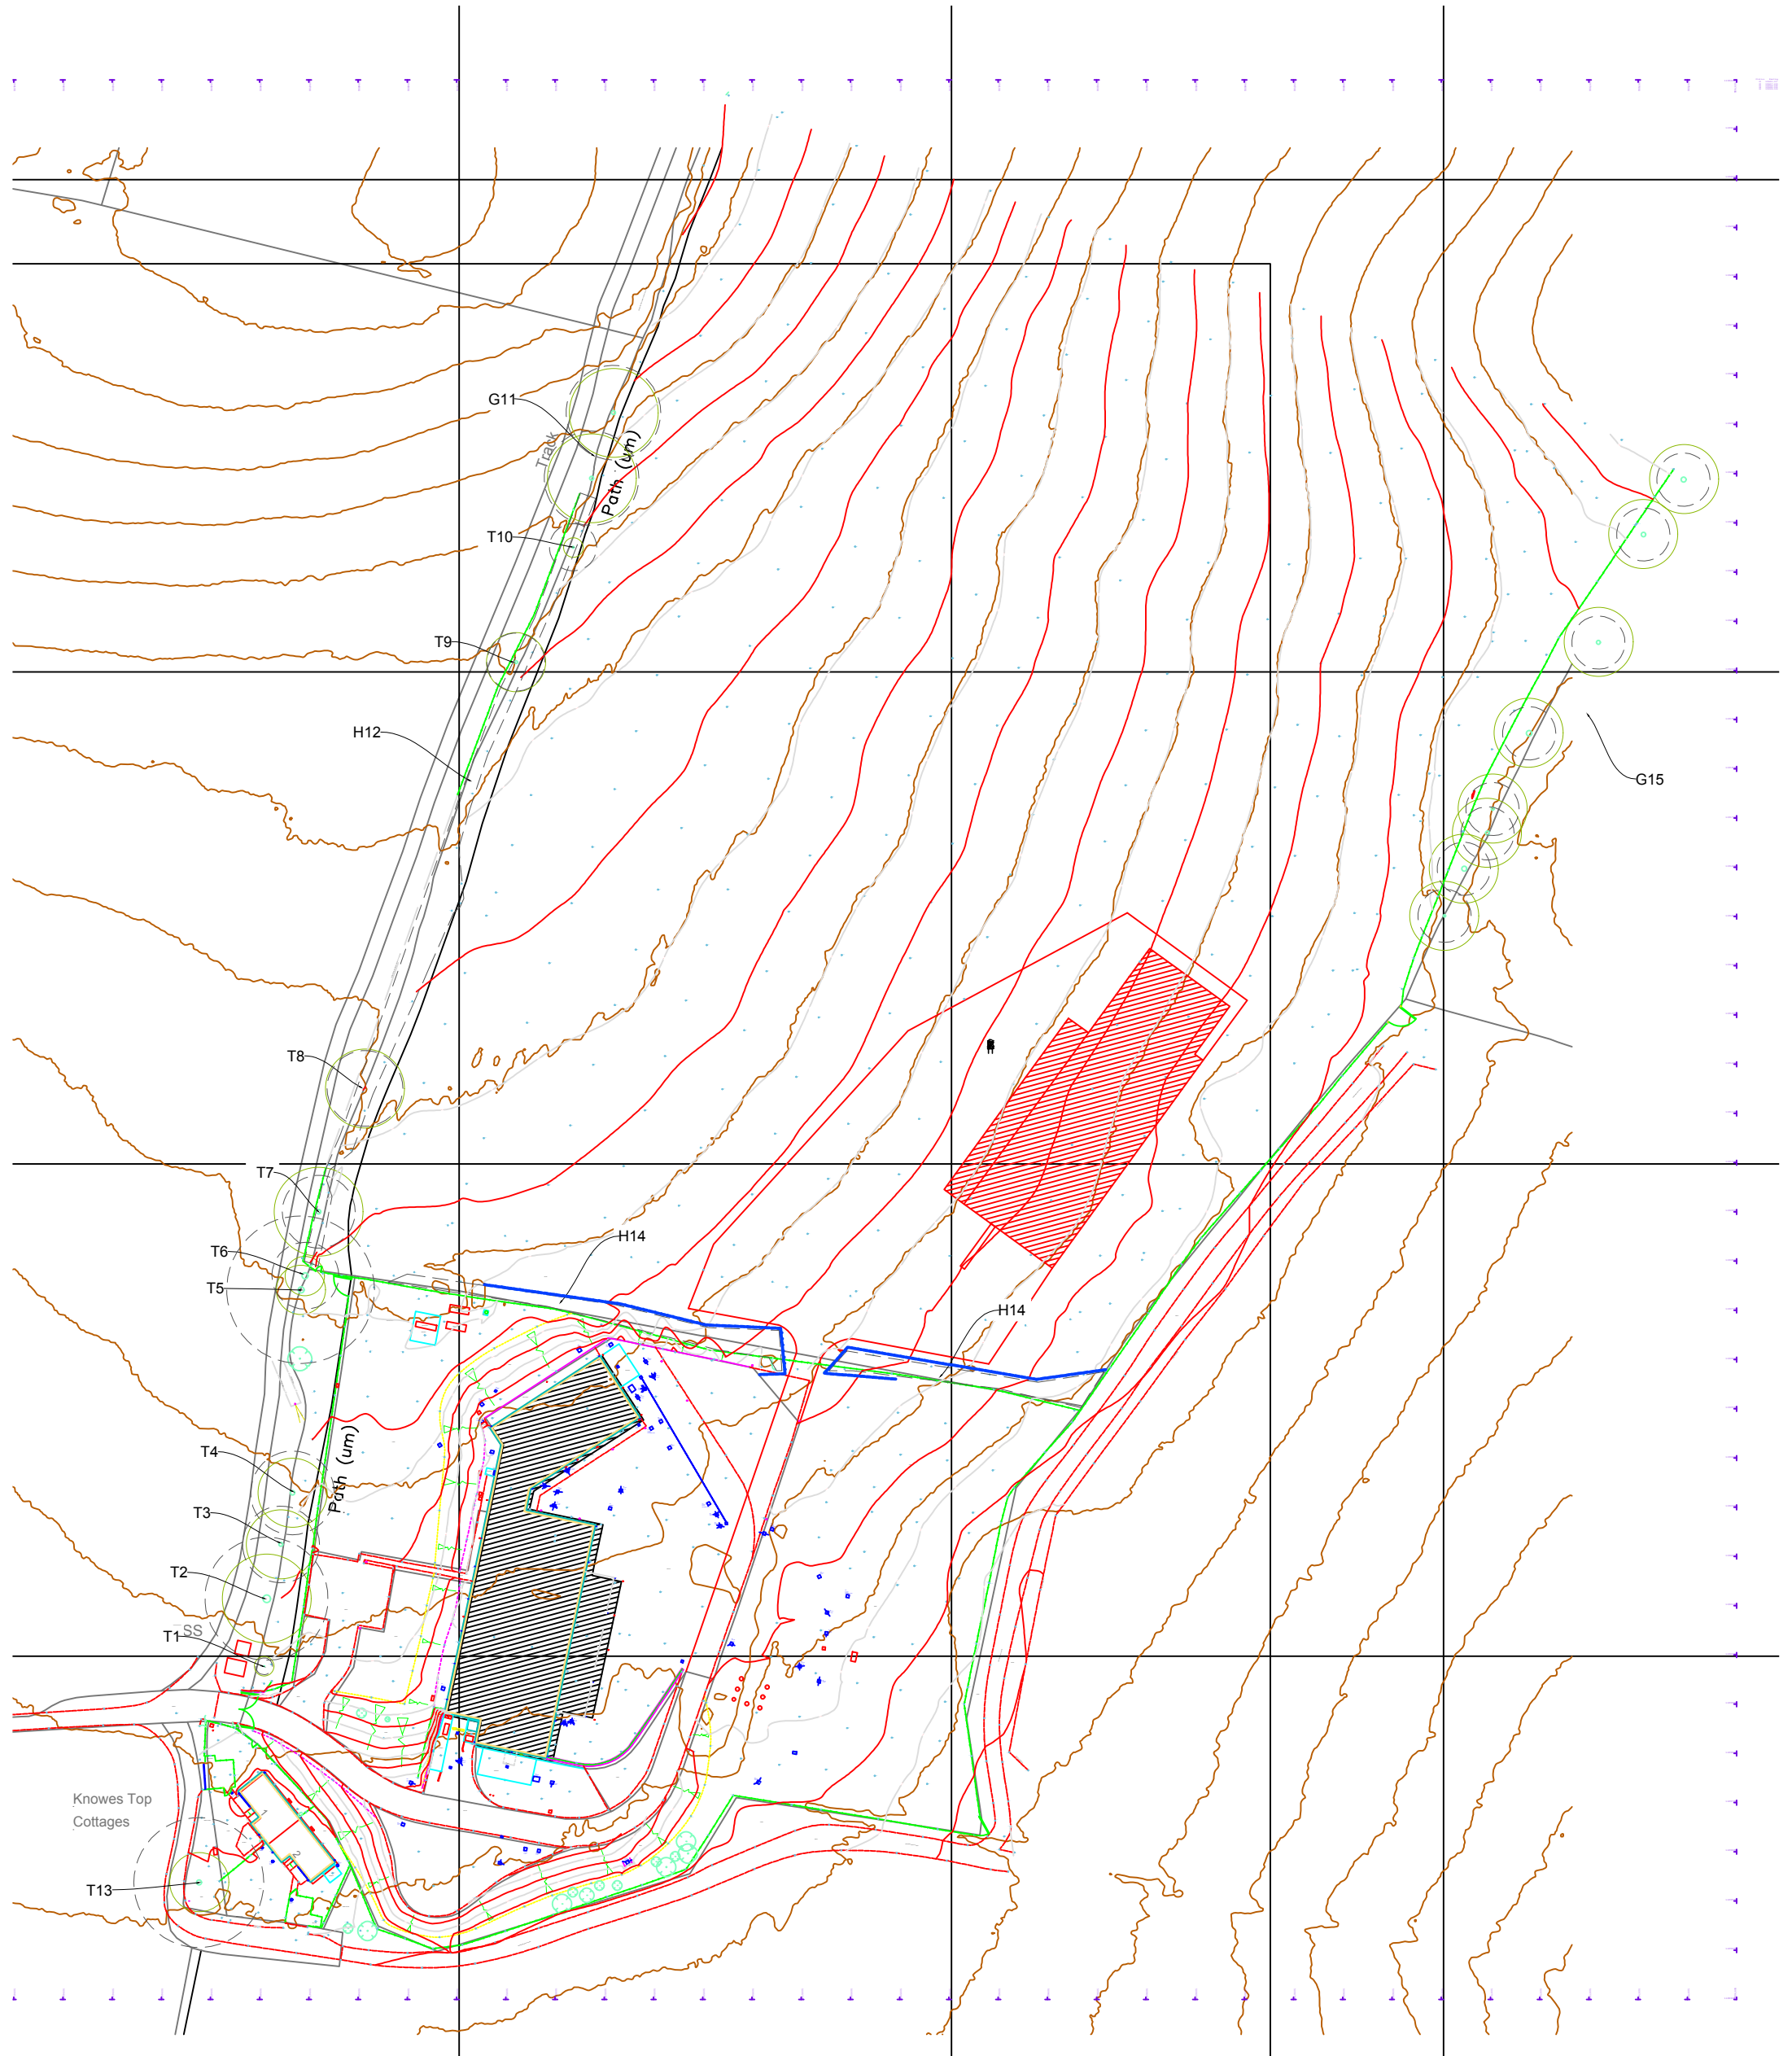

Tree Survey Schedule contained within the arboricultural report ref. PJC/7212/26-02 contains further information for each tree.


This drawing should be viewed in colour.

- Key:**
-  RPA for tree to be retained
 -  Canopy of tree to be retained
 -  Tree protection fencing


Drawing no: PJC/7212/26/C	Rev: -	Sheet number: 1 of 1
Client and site: ECE Planning		
Knowe Top Farm West Chiltington West Sussex		
Drawing title: Tree Protection Plan		
Date drawn: 25/06/2026		
Scale: 1:1250 at A3		
Drawn by: NB	Checked by: PD	



Appendix 5: Tree Protection Fencing Specification

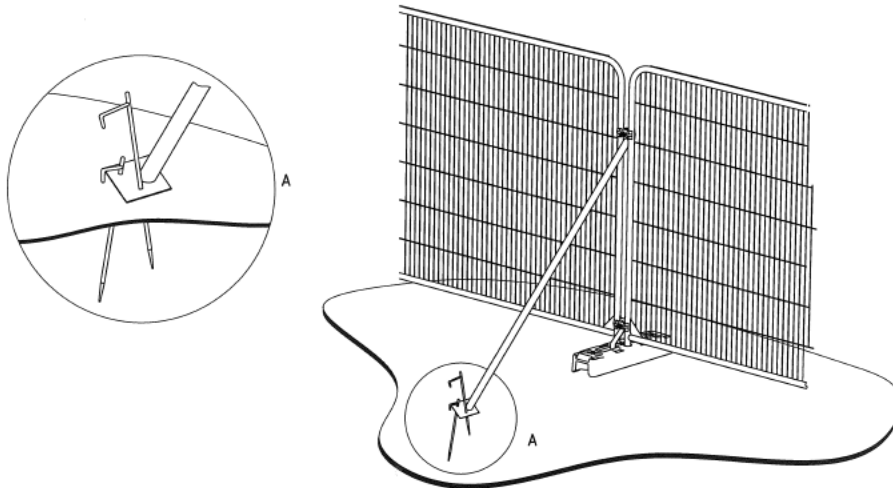

a) Stabilizer strut with base plate secured with ground pins

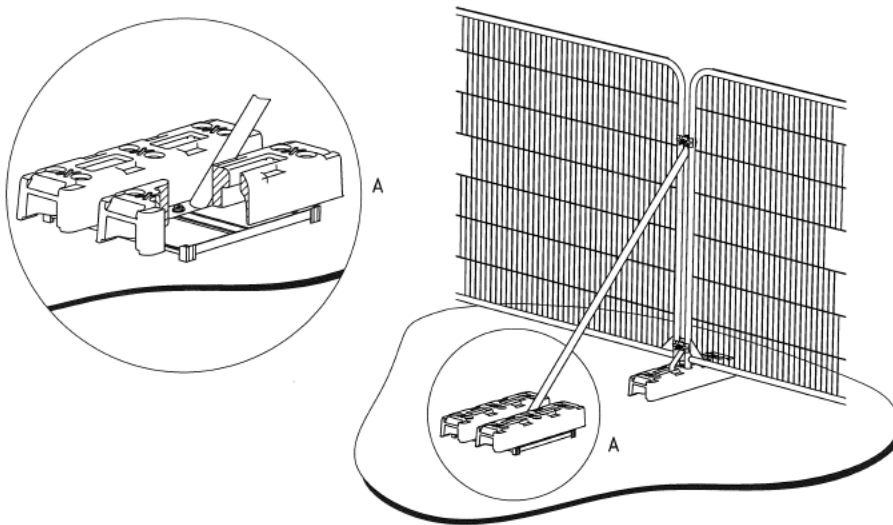

b) Stabilizer strut mounted on block tray



Appendix 6: Example Protective Fencing Sign





CONTACT DETAILS

Kent Office:

The Watermill
The Mill Business Park
Maidstone Road
Ashford
Kent
TN26 1AE

Tel: 01323 832120

Tel: 01233 225365

Author: Nick Betts

Date: 25th June 2026

E-mail: nick@pjconsultancy.com
