


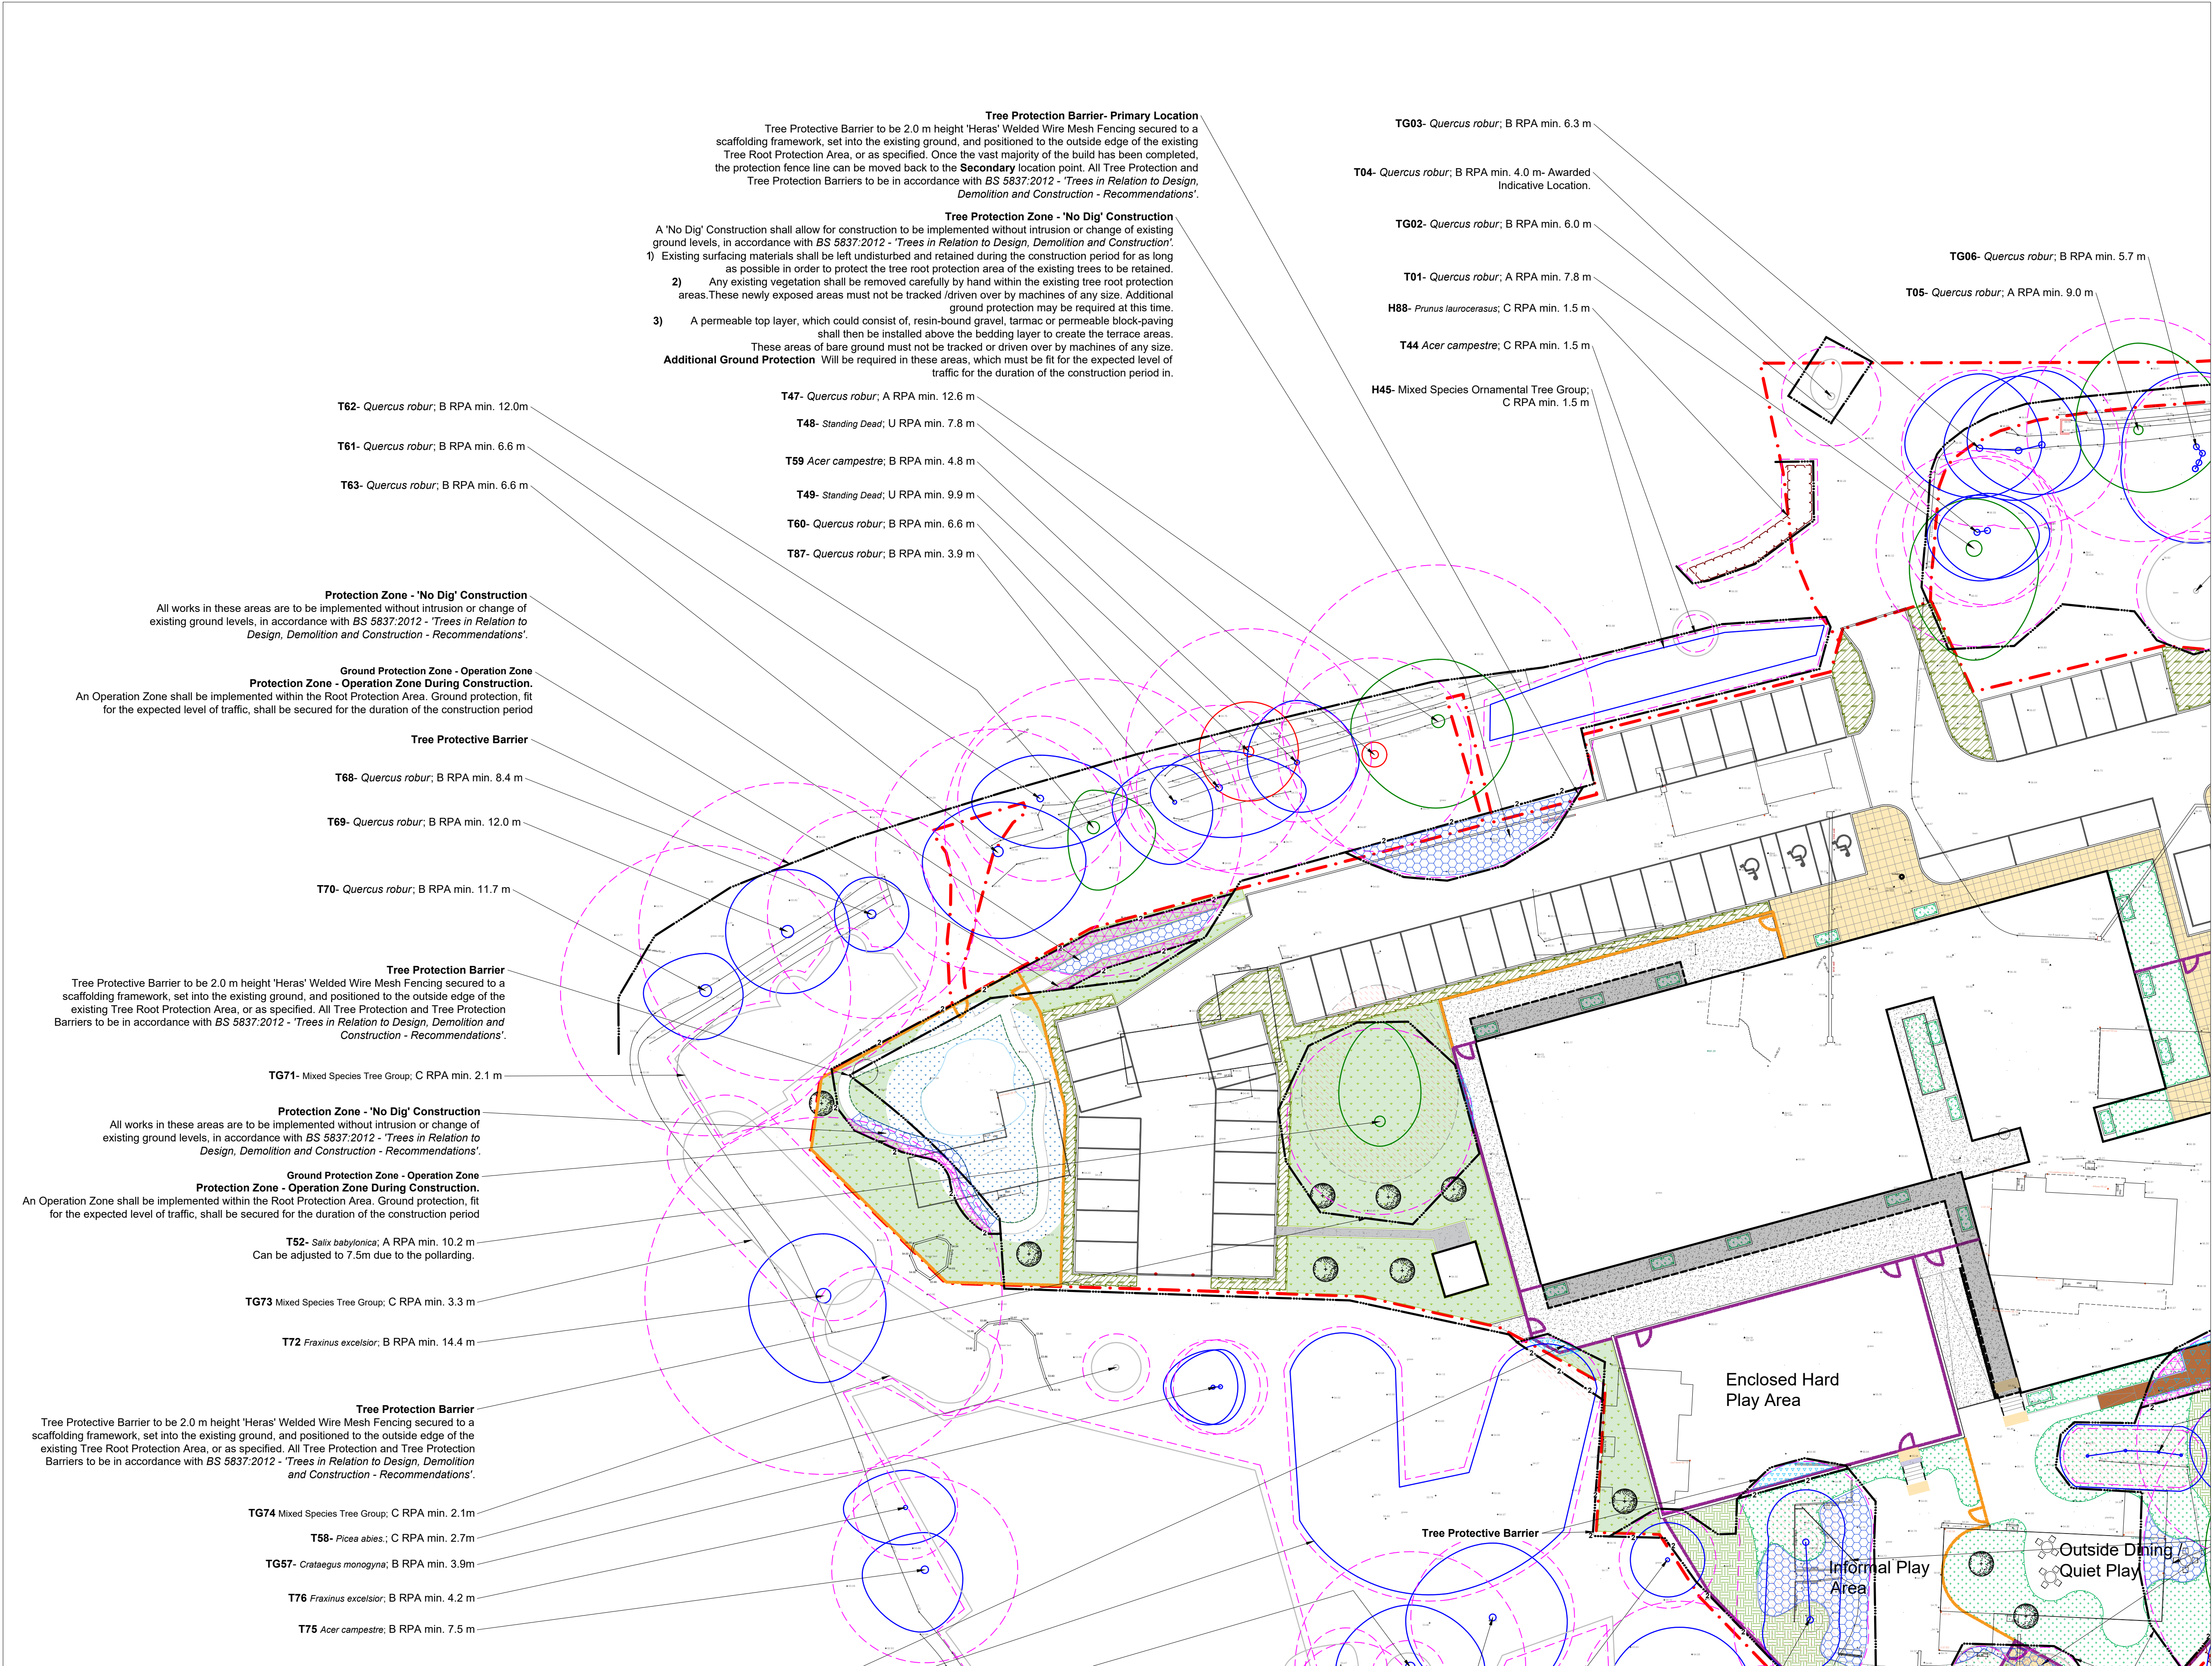

Legend

T02

Tree, Hedgerow and Shrub Numbers.

Tree Root Protection Areas
Specified in accordance with BS 5837:2012 - 'Trees in Relation to Design, Demolition and Construction - Recommendations'.

Category A Trees
Trees of High Quality and Value to be Retained.

Category B Trees
Trees of Moderate Quality and Value to be Retained.

Category C Trees
Trees of Low Quality and Value to be Retained.

Category U Trees
Trees unsuitable for long term retention.

Existing Trees to be Removed
All operations to be in accordance with BS3998:2010- 'Tree Works- Recommendations'

Existing Shrubs and Hedges to be Removed

Tree Protection Barrier
All Tree Protection Barriers to be in accordance with BS 5837:2012 - 'Trees in Relation to Design, Demolition and Construction - Recommendations'.
2.0 m height 'Heras' Welded Wire Mesh Fencing secured and positioned as specified.

2nd Location- Tree Protection Barrier
This is the secondary location of the protection fencing. Once the vast majority of the build has been completed, the protection fence line can be moved back to this point to allow the implementation of Soft Landscaping.

Protection Zone - 'No Dig' Construction
Works to be implemented without intrusion or change of existing ground levels, in accordance with BS 5837:2012 - 'Trees in Relation to Design, Demolition and Construction - Recommendations'.

Protection Zone - Operation Zone During Construction.
An Operation Zone shall be implemented within the Root Protection Area. Ground protection, fit for the expected level of traffic, shall be secured for the duration of the construction period

Protection Zone - Manual Excavation
A Limited Manual Excavation shall be implemented, in accordance with BS 5837:2012 - 'Trees in Relation to Design, Demolition and Construction - Recommendations'. All works in these areas shall be undertaken with due care with hand held tools under Arboricultural Supervision only.

Notes:

- Drawing to be read in colour.
- For details of existing trees and vegetation refer to: LLD3660-ARB-SCH-001 - Existing Tree Schedule;
- For assessment of effects of the proposed development on existing trees refer to LLD3660-ARB-REP-001- Arboricultural Impact Assessment and Method Statement.

PLANNING ISSUE

Rev	Description	Date	Initials
03	Planning Issue	13.03.26	GO
02	Draft Issue	13.01.26	RM
01	Draft Issue	08.01.26	GO
00	Draft Issue	06.01.26	GO

LIZARD

Landscape Design and Ecology

The Old Bank, 34 South Street, Tarring, Worthing, West Sussex, BN14 7LH
T. 01903 216033 E. lizardlandscape@btconnect.com W. lizardlandscapeology.com

Client
Salutem Shared Services

Project Title and Location
Woodview School on Ingfield Manor School.
Manor Drive, Five Oaks, Billingshurst RH14 9AX

Drawing Title
Tree Retention and Protection Plan

Scale 1:250@A1	Drawn GO	Approved KM	Date 06/01/2026
Drawing No LLD3660-ARB-DWG-020	Revision 03		

Tree Retention and Protection Plan

South Side- Ingfield Manor Drive, Five Oaks, Billingshurst RH14 9AX
