
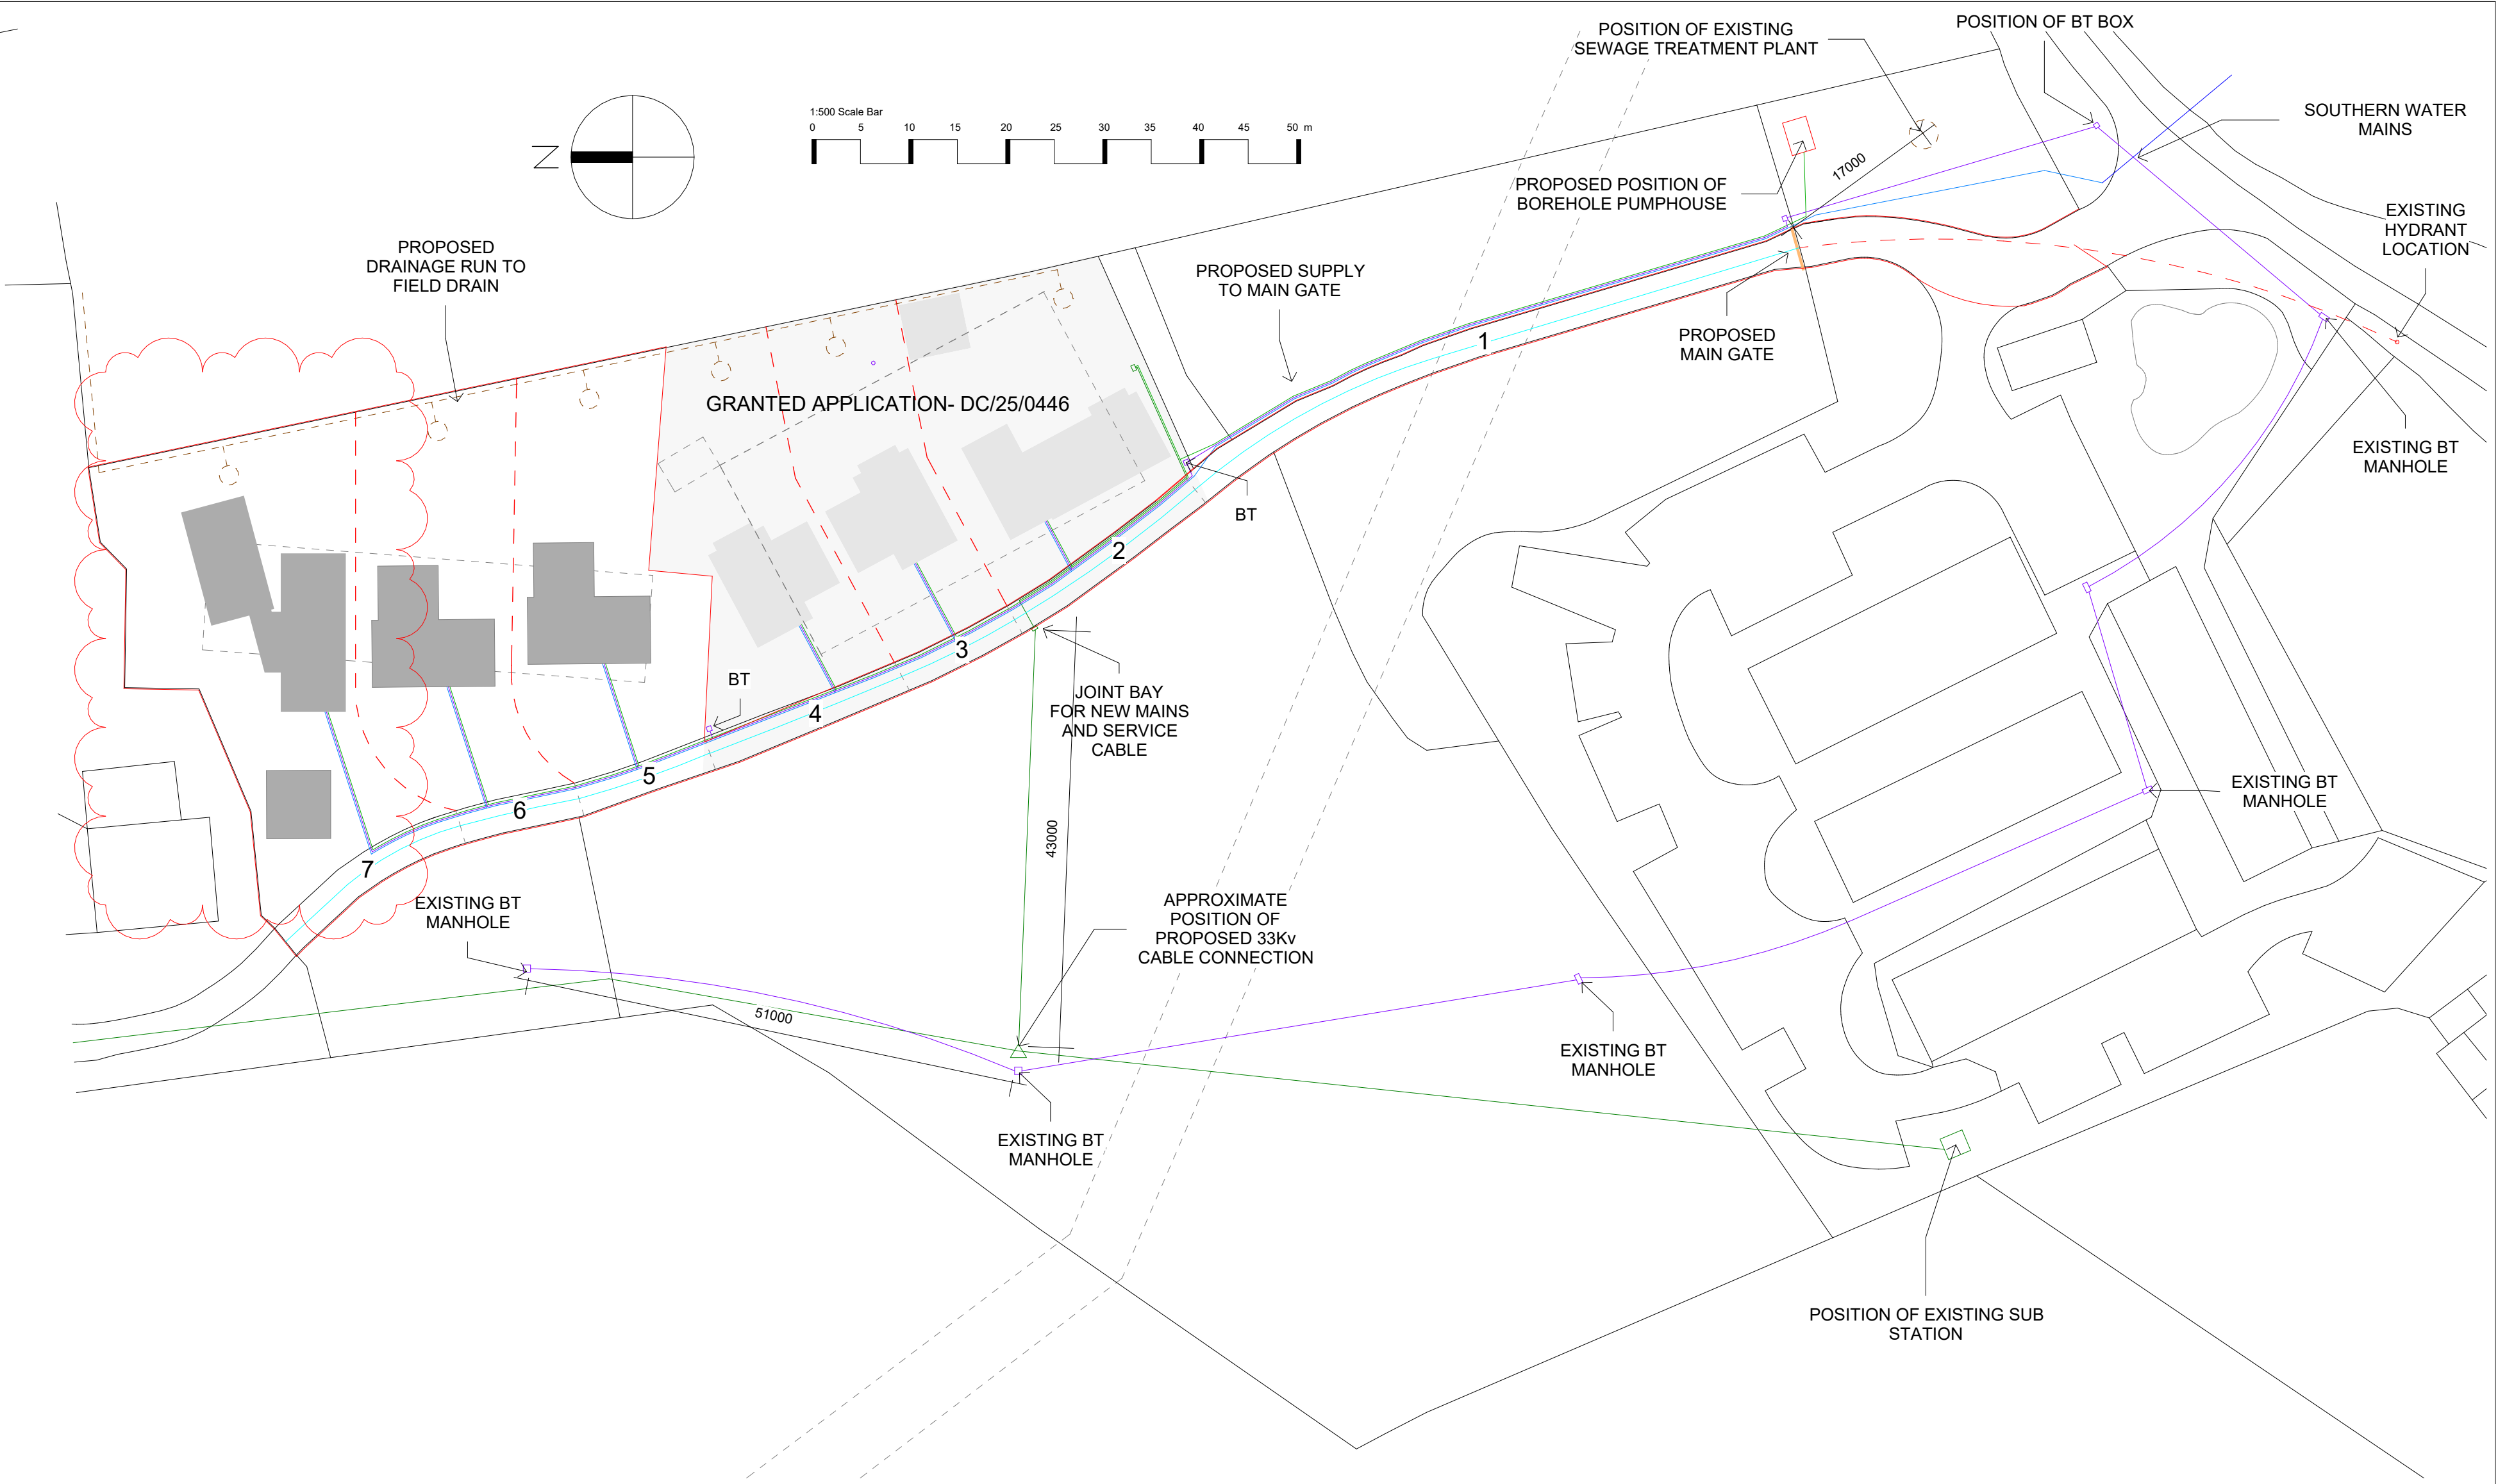


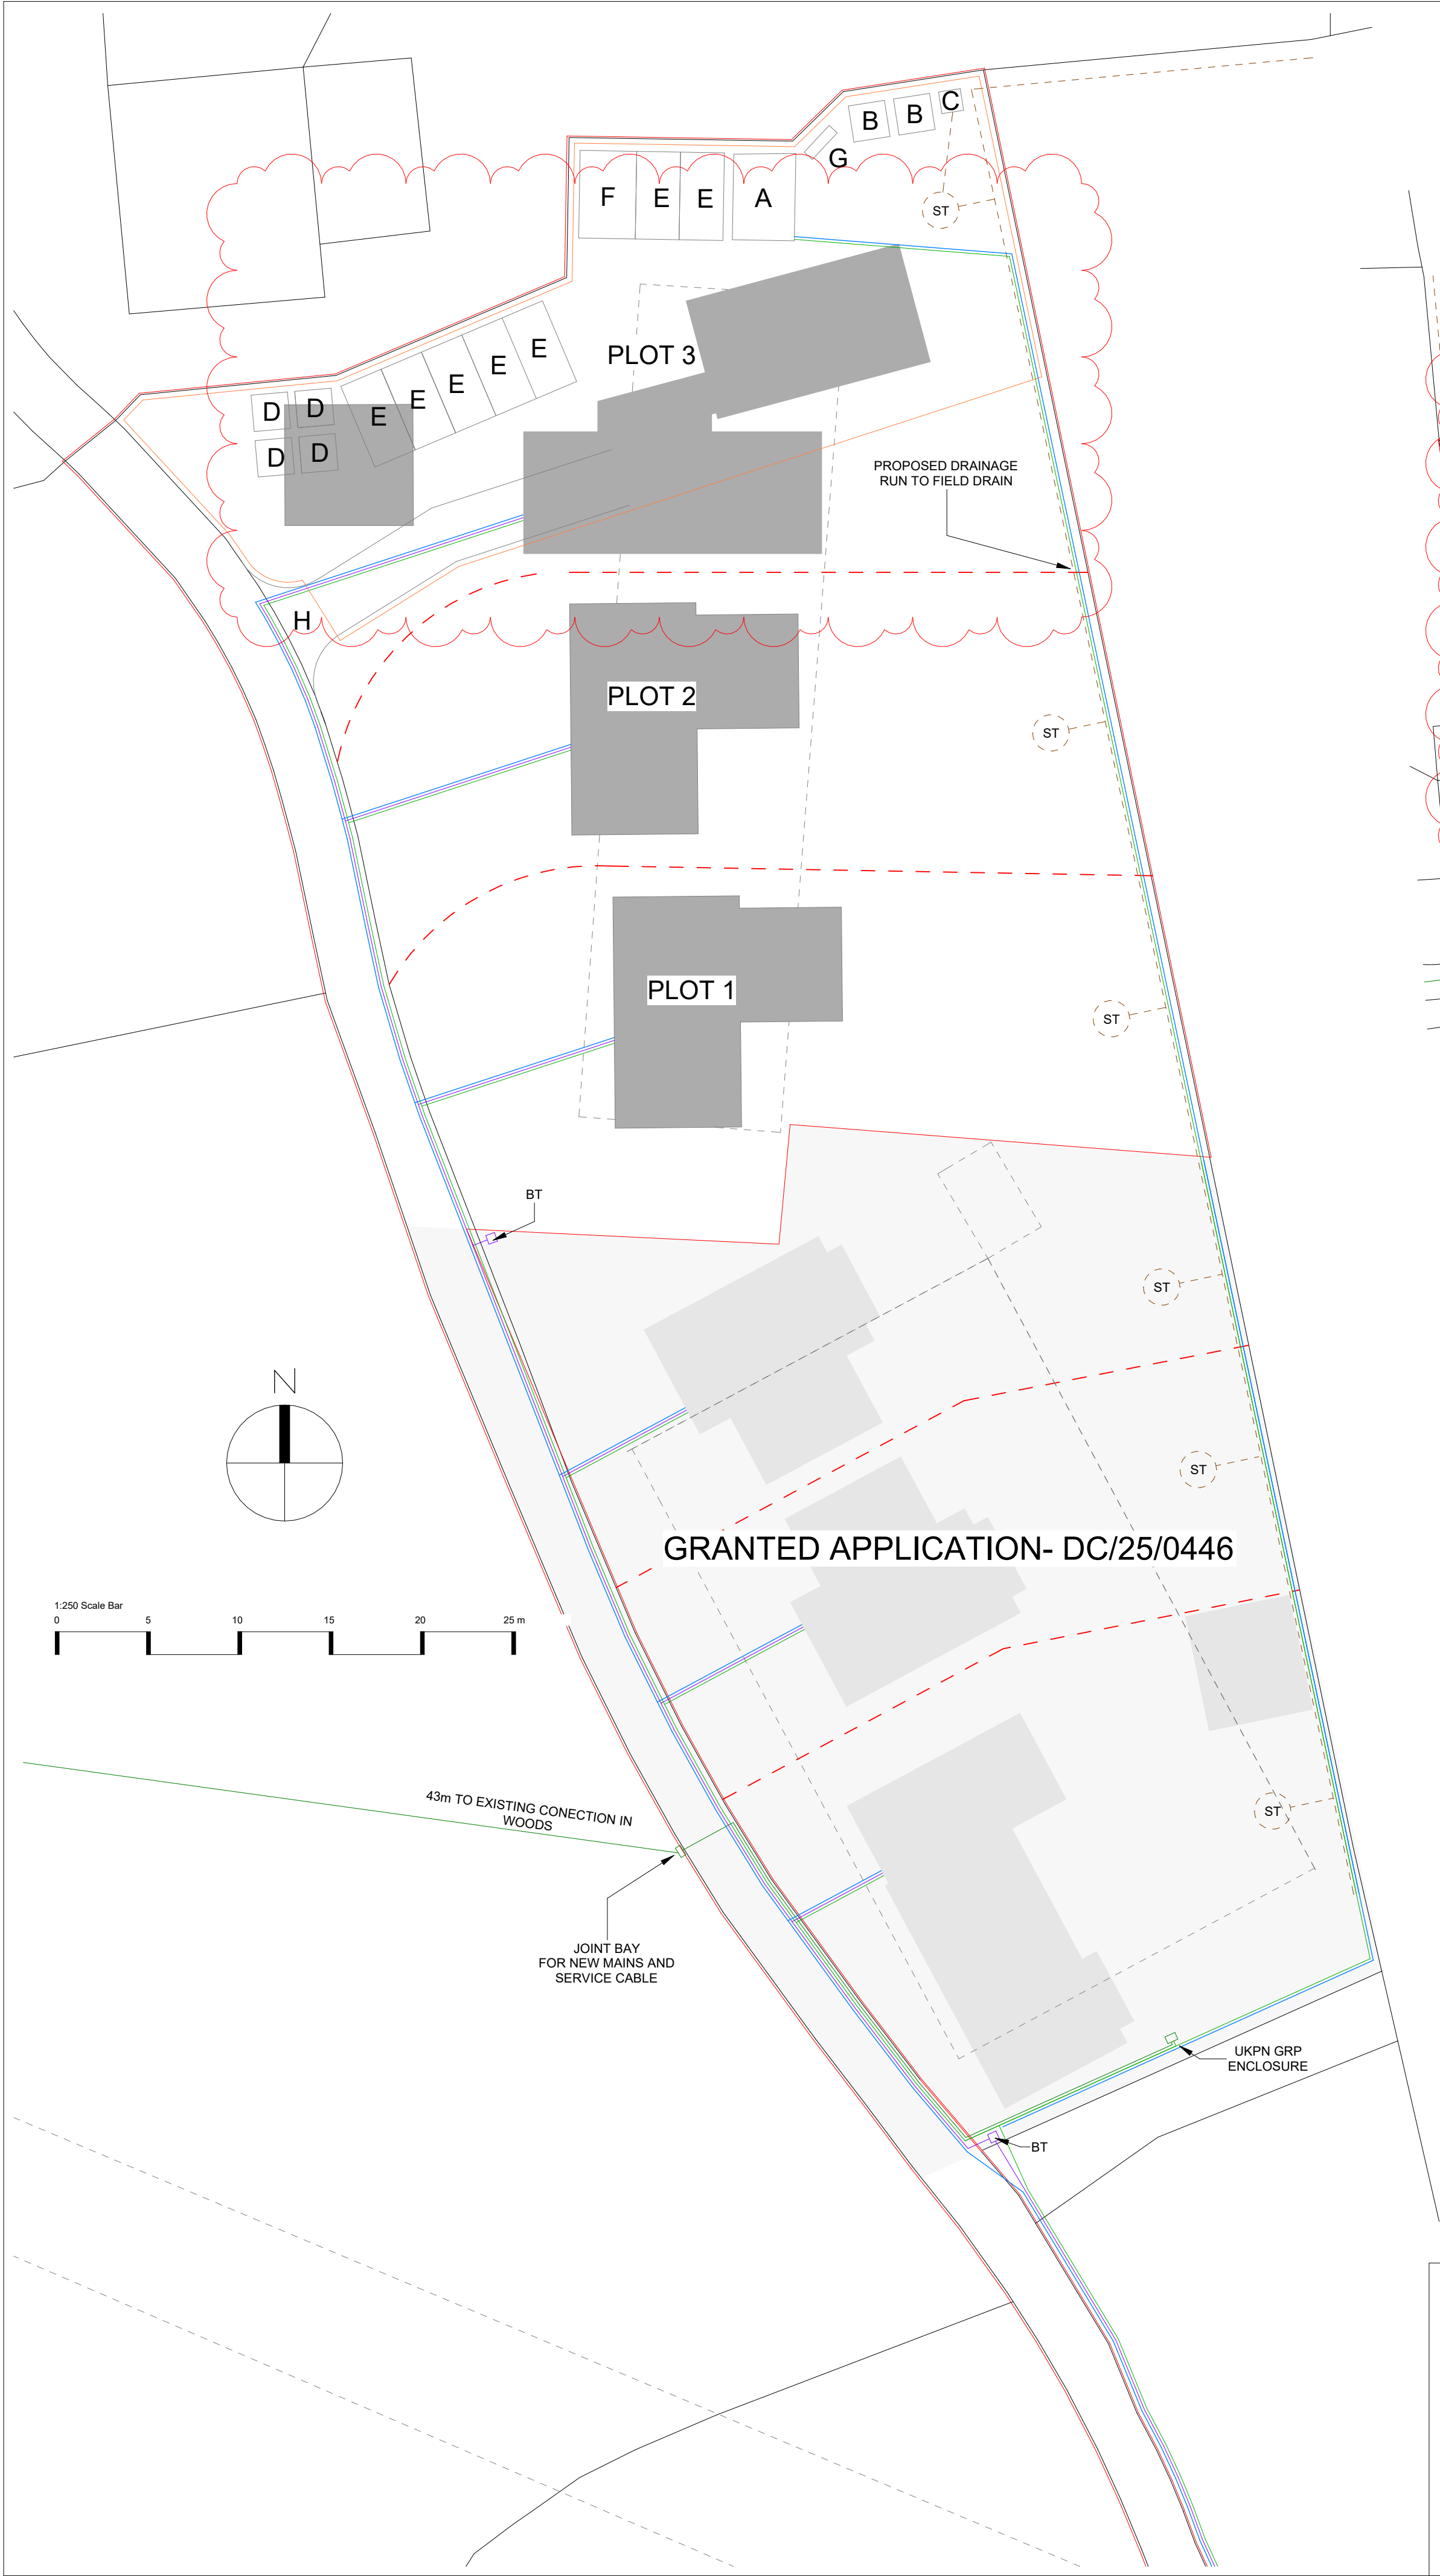



- A. SITE WELFARE BUILDING
- B. 2m X 2m STORAGE CONTAINERS
- C. SITE TOILETS
- D. UNLOADING AND MATERIAL STORAGE AREA
- E. SITE PARKING
- F. HEAVY PLANT PARKING AREA
- G. TOOL CLEANING
- H. SECURE COMPOUND ACCESS
- PROPOSED SITE HOARDING

ACCESS ROAD DISTANCES	
1.	67,744
2.	22,983
3.	13,024
4.	21,344
5.	14,293
6.	12,570
7.	21,910

DISTANCES FROM HYDRANT TO FAR END OF PLOT ALONG ACCESS ROAD	
PLOT 1.	202,638
PLOT 2.	215,208
PLOT 3.	237,118
TO GATE	63,250

- WATER - CONNECTIONS TO BE TAKEN THROUGH THE GATE AREA TO KEEP THE SUPPLY RUNNING ALONGSIDE THE DRIVEWAY TO THE FRONT OF THE HOUSES. POTENTIAL HYDRANT REQUIRED.
- ELECTRICITY - TAKEN FROM THE EXISTING SUPPLY IN THE WOODS TO THE GRP BOX FOR A SUPPLY TO THE MAIN GATE.
- ELECTRICITY - 3 NEW SUPPLIES TO BE TAKEN TO THE HOUSES.
- BT - PROPOSED ROUTE MARKED - TO BE CONFIRMED BY OPENREACH
- DRAINS, SOAKAWAYS AND SEWAGE TREATMENT PLANTS

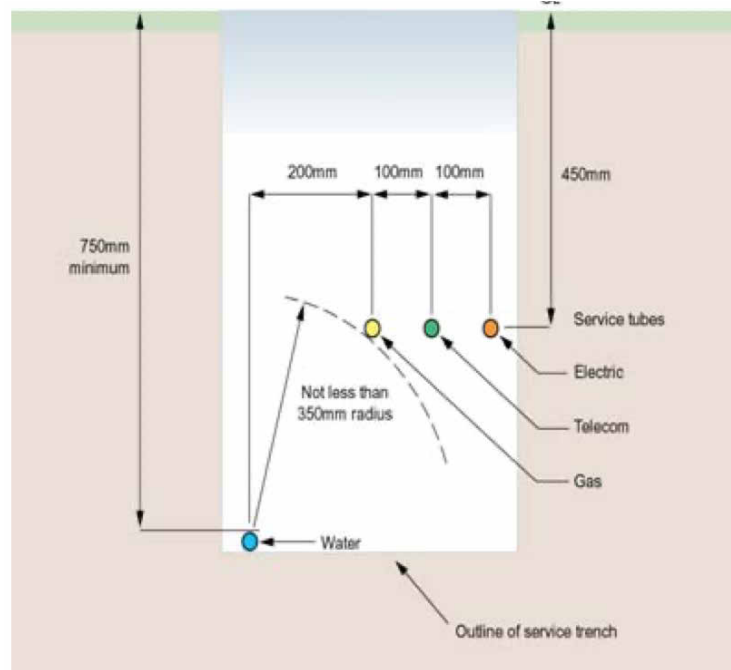

Revision	Description	Date	Drawn	project	Long Barn, Crays Lane, Goose Green, RH20 2LR	 New Form Architecture your vision delivered 5 The Cairns Charlestown, Fife, K11 3EP tele 07843022953 email info@newformarchitecture.com web www.newformarchitecture.com			
				client	Tri-Star Fire				
				title	Proposed Site Services				
				status	PLANNING				
1	House Type 2 Layout amended to reduce impact on RPA.	14.05.25	AM	scale	As indicated@A1	drawing number	PL-GA-13	rev	1
