
Default Barrier Specification, cited BS 5837:2012

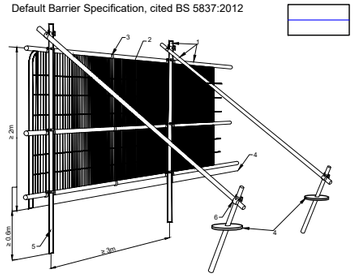

Key
1 Standard scaffold poles
2 Heavy gauge 2m tall galvanized tube and welded mesh infill panels
3 Panels secured to uprights and cross-members with wire ties
4 Ground level
5 Uprights driven into the ground until secure (minimum depth 0.6m)
6 Standard scaffold clamps

1:500 @ A3

0m 5m 10m 20m

KEY:

- Site Boundary
- 15 Tree Numbers
- Tree Canopies
- [8] Category 'U' Trees
- Category 'A' RPA
- Category 'B' RPA
- Category 'C' RPA
- Tree Protection Barrier

Note: Trees T15, T16 & T17 have been plotted using measurements onsite in conjunction with aerial imagery. Their locations were not recorded on the topographical survey of the site (drawing ref: 240023-A-P-PL_RIBA03.dwg).

T14 T15 T13 T12 [T17] T11 [T10] T9 T16 T8 T7 T6 T5 T4 T3 T2 T1

A272 Hilland Road

Newman Way

Balancing Pond

43 x 2.4m sightline

Shared surface

Plot 1

4.1m wide access road

1.8m cb fence

1.8m brick wall

Retaining wall

+40.00 FFL

4b

Turning Head

Shared surface

3b

+42.50 FFL

+42.25 FFL

Plot 2

Plot 3

Plot 4

Plot 5

Plot 6

Future 'estate' landscaping along boundary

Old

REV	DATE	NOTE	Drawn

REVISIONS

aspect arboriculture

TITLE
Hilland Road, Billingshurst
Tree Protection Plan

CLIENT
Roddy New Homes

SCALE	DATE	DRAWN
1:500 @ A3	SEP 2025	JB

DRAWING NUMBER	REVISION
12663 TPP 01	

Based on: 240023-A-P-PL_RIBA03
