Land Science

ROWFOLD LODGE, CONEYHURST ROAD, BILLINGSHURST

REMEDIATION METHOD STATEMENT

MR A. RUTHERFORD

18TH NOVEMBER 2024

LS8077

Site:	**ROWFOLD LODGE, CONEYHURST ROAD, BILLINGSHURST**
Title:	**REMEDIATION METHOD STATEMENT**
Project:	**CONVERSION OF A REDUNDANT AGRICULTURAL BUILDING INTO A SINGLE STOREY, ONE-BEDROOM, RESIDENTIAL DWELLING WITH PRIVATE GARDENS**
Client:	**MR A. RUTHERFORD**
Date:	**18TH NOVEMBER 2024**
Reference:	**LS8077**
Version:	**A – final for issue**

Prepared By:	[redacted]	**JOCELYN MIDDLETON** MGeol FGS **Principal Geo-Environmental Consultant**
Checked and Authorised By:	[redacted]	**MICHAEL ROSE M.Sc., B.Sc., FGS, AIEMA** **Principal Geo-Environmental Consultant**

Land Science are Geotechnical Engineering and Contaminated Land specialists for construction, regulation, property ownership, and due diligence. By understanding our client's needs and appreciating the role that ground issues play within a wider context, we provide a reliable service and first-class expertise tailored to specific requirements. For more information on how we can benefit your project, please visit www.landscience.co.uk

CONTENTS

1.0 INTRODUCTION 4
2.0 REMEDIATION OBJECTIVES AND OPTIONS 6
3.0 GEO-ENVIRONMENTAL DISCUSSION 7
4.0 IMPLEMENTATION PLAN 8
5.0 SITE CONTROLS 12
6.0 VALIDATION REPORT REQUIREMENTS 13
REPORT CONDITIONS 15
GLOSSARY OF TERMS 16

FIGURES

FIGURE 1: Site Location Plan
FIGURE 2: Existing Layout
FIGURE 3: Proposed Layout

APPENDICES

APPENDIX A: Terram Hi-Vis Geotextile
APPENDIX B: Screening Criteria

1.0 INTRODUCTION

1.1 General

Land Science was instructed to undertake a Remediation Method Statement in relation to the change of use with a proposed single dwelling residential development at Rowfold Lodge, Coneyhurst Road, Billingshurst, RH14 9DD. The location is shown on Figure 1, which is centred at grid reference TQ 09894 25486.

1.2 Client

The Client for this appointment was Mr A. Rutherford. This report may only be used by this named client and their project team for the purposes set out and subject to the report conditions. It was understood that the Client already owned the property, and that this investigation was not a pre-purchase appraisal.

1.3 Area Under Investigation

The area under investigation comprised a small redundant former agricultural building situated approximately 50m to the south of Rowfold Lodge. The layout is indicated on Figure 2, and the area was approximately 1.7 hectares.

1.4 Proposed Development

The proposed development was understood to comprise the conversion of a redundant former agricultural building to a small single storey, one bedroom, residential dwelling, with space for private gardens. The proposed development was covered under planning application number DC/24/0304. Figure 3 illustrates the layout of the proposed redevelopment. The findings of this report may not be valid if the proposed development is altered.

1.5 Previous Investigations

The following previous investigations relevant to the site were made available:

- Phase I Geo-Environmental Assessment, ref. LS7634, by Land Science, dated May 2024.
- Main Investigation Report, ref. 21591/MIR Rev 1.0, by Soils Limited, dated October 2024.

This Remediation Method Statement is based on the findings and recommendations within the above reports. The RMS may require amendments following the review by the Contaminated Land Officer at Horsham District Council.

1.6 Scope of Work

Land Science were instructed to carry out a Remediation Method Statement, in relation to removing/reducing any potential risks to any sensitive receptors.

1.7 Standards

Where practicable, the investigation was undertaken in accordance with the following primary standards and guidance:

- Land Contamination Risk Management (LCRM) Environment Agency 2020.
- BS10175:2011+A1:2013, Investigation of Potentially Contaminated Sites.
- National Planning Policy Framework, July 2018.
- Building Regulations Approved Document C: Site preparation and resistance to contaminants and moisture, HM Government, July 2013.
- NHBC Standards Chapter 4.1: Land Quality - Managing Ground Conditions, 2019.

Other technical sources have been cited in respect of specific aspects of the investigation, as referenced throughout the text.

2.0 REMEDIATION OBJECTIVES AND OPTIONS

2.1 Objectives

The distribution, nature and concentrations of contaminants of concern are a critical consideration for the selection of the correct remedial technology for the attainment of the remediation objectives.

The prevalence of some recalcitrant contaminants may make a specific technology expensive or unviable in terms of treatability and/or cost. The selection of the right remedial technology is further complicated by other considerations such as the geological and hydrogeological setting, extent of previous investigation/remediation works, the time available for implementation and treatment, site access and restrictions posed by ongoing development, and cost.

The primary objective of the remediation activities will be for the safe redevelopment of the site that is suitable for the proposed end-use. Considering the previous sections, the following remedial options available to manage unacceptable risks will either:

- Manage (remove, destroy, modify or immobilise) the source;
- Interrupt the pathway; or
- Modify the receptor or the behaviour of the receptor.

The preferred options will be designed to manage the source of contamination or interrupt the pathway.

Source management may involve the removal, destruction, or transformation of the source. Pathway interruption may involve either the blocking of the pathway or the destruction or removal of contaminants moving along a pathway.

This can be achieved either via the permanent reduction of contaminant concentrations to acceptable limits; source removal; pathway interruption.

2.2 Constraints

There are limited constraints at the site, proposed site levels could be raised / lowered slightly if needed, material could be reused on site and excavated natural soils could be stockpiled on site for future use as backfill.

3.0 GEO-ENVIRONMENTAL DISCUSSION

The previous Main Investigation Report (21591) undertaken by Soils Limited identified some risks to receptors at the site including:

- Exceedances of Polycyclic Aromatic Hydrocarbons (PAHs) at HDP2 at 0.20m, in an area of proposed soft standing. The exceedances included benzo(b)fluoranthene, benzo(a)pyrene and dibenz(a,h)anthracene, which were higher than the Residential with home grown produce screening criteria (GAC).

Soils Limited recommended that the position HDP2 be treated as a hotspot and that a remediation strategy was required to remove the PAH risk.

With respect to PAHs, Land Science adopt the surrogate marker approach described in Appendix E of the C4SL suite of documents i.e. using benzo(a)pyrene as a representative compound for all genotoxic PAHs. This approach was used as benzo(a)pyrene [B(a)P] was detected in the samples, and the other PAHs identified above the individual screening values were all classed as genotoxic. The GAC for B(a)P is 5.0mg/kg and the sample exceeded the threshold with a value of 6.26mg/kg.

However, Land Science consider that the PAH exceedances may have resulted due to the tarmacadam identified within the Made Ground. It was also recorded in HDP1, HDP3 and HDP4. The chemical results confirm that some of these PAH results are close to the screening threshold criteria.

In addition, the physical composition of the Made Ground on site (with bricks, concrete, flint and little soil) was such that it was unlikely to be a suitable medium for landscaping and planting. Clean imported topsoil and subsoil will be required in accordance with appropriate British Standards.

4.0 IMPLEMENTATION PLAN

Following the discussion in section 3 the preferred remediation options are as follows: -

- Excavating and disposing of poor-quality soils (Made Ground) from the proposed soft landscaping areas and replacement with a capping system comprising imported topsoil / subsoil (minimum 150mm but dependent on type of vegetation to be grown).
- Waste Disposal considerations.
- A Discovery Strategy should also be followed during the development.

The following strategy has been prepared in order to render the site safe for residential occupation.

It is considered that site levels will remain unchanged and the proposed soft landscaping areas will require remediation. This will comprise the removal of all existing surface Made Ground in the proposed soft landscaped areas to the depths discussed in the following sections and replacement with clean imported topsoil / subsoil.

The following sections 4.1 and 4.2 give specific details relating to the proposed soft landscaping areas for the site.

4.1 Landscaped Areas

It is understood that the proposed landscaping areas are for a residential end-use with potentially grass, shrubs and trees. Full landscaping details have not been provided by the client, but the new soil make up (topsoil and subsoil) in these areas should be to the specified depths as per the type of vegetation to be grown, comprising the following from existing ground level:

- 150mm – grass
- 600mm – shrubs
- 900mm - trees

If any Made Ground is found to be present below this depth, then a geotextile membrane (e.g. Terram Hi-Vis) should be placed between any Made Ground and imported soils, to prevent migration/mixing. The data sheet for the Terram Hi-Vis Geotextile is contained within Appendix A.

Proposed finished levels are assumed to be the same as the existing site levels. Any Made Ground excavated should be disposed of appropriately off site.

4.2 Imported Materials

Material used to raise site levels must be suitable for the proposed end use and chemical testing is recommended to confirm that they do not contain elevated concentrations of potential contaminants of concern that could pose a risk to end users (e.g. asbestos). Testing should meet the screening criteria appended to this document (Appendix B) and must be 'clean' and 'suitable for use' with no visual evidence of contamination (sharps or visual signs of pollution).

The soil testing requirements for any imported backfill materials should be as follows: -

Soil Type	Chemical Testing	Required Testing Frequency
Imported Topsoil	pH, Soil Organic Matter, Heavy Metals, PAH, BTEX, Asbestos Screen + BS3882:2015 physical testing for topsoil.	On site: 1no. sample per 50m³ for each material and source.
Subsoil	pH, Soil Organic Matter, Heavy Metals, PAH, Asbestos Screen + BS8601:2013 for subsoil.	Where >10m³ a minimum of 3no. samples.

In addition, the laboratory test results for material imported to soft landscaping areas should also meet the criteria in the following table with respect to potential phytotoxic risk to plant growth.

Element	Phytotoxicity Value (mg/kg)			Arable (grassland)
	pH <6.0	pH 6.0-7.0	pH >7.0	pH >5.2
Zinc	200	200	300	300 (300)
Copper	100	135	200	200 (330)
Nickel	60	757	110	110 (180)
Cadmium	50*			3.0 (3.0)
Arsenic	1,000*			50 (50)

If the verification tests fail screening criteria, then the material is deemed not acceptable and should be removed from site.

Records of the volume of imported materials will be kept (transfer notes / purchase records) and a summary table (with volumes, dates removed and waste classification) will be included within the Validation Report. The summary will also have a calculation to show the volume of material removed from the proposed landscaped areas corresponds to the same volume of imported subsoil / topsoil this is to confirm that enough 'clean' imported material has been brought onto the site to infill any excavations and that site won materials have not been re-used.

The removal of Made Ground and the provision of chemically suitable material should be monitored and validated by a suitably qualified environmental consultant with detailed site inspection sheets compiled (confirming details of areas inspected, depths of any imported soils, samples taken and where any further work is required etc.). Photographs will be taken and included with the inspection sheets in the Remediation Validation Report.

4.3 Waste Management

4.3.1 Stockpiles

If material is excavated from the ground (e.g. site strip and service trenches) it may be stockpiled on site. If stockpiles are to be created, they should be on impermeable ground, over a geotextile membrane and managed suitably to minimise dust generation i.e. dust suppression and suitable covers. Stockpiles must be bunded to prevent possibility of contaminated surface water run-off impacting surrounding land.

Stockpiles of 'waste arising' for offsite disposal and stockpiles of imported 'clean' material for use as anti-dig / clean capping need to be clearly marked and appropriately segregated to avoid the potential for cross contamination.

Stockpiles should be regularly surveyed and records maintained to be included in the validation report.

The Contractor undertaking the remediation works is responsible for compliance with waste management legislation where issues relating to waste arise as a result of the works. As a minimum, the following is required:

- Management of material that arises during the works and is classified as waste.
- Waste streams are appropriately classified prior to offsite disposal.
- Audit process for the selection of waste management contractors to include the collection and assessment of licences, permits and registrations.

4.3.2 Soil Disposal

The contractor should allow for a suitable regime of testing soil arisings to ensure they are being disposed of to the appropriate facility with the appropriate level of duty of care.

The results of the soil analysis recently carried out by Soils Limited can be used for this classification.

The receiving waste facility should be consulted as they may be able to handle different wastes with higher acceptance criteria.

Further WAC testing may be considered for soils identified as Non-Hazardous, as the tests may enable those materials to be re-classified as Inert and therefore represent a potential saving on disposal costs.

Liaison with the proposed receiving facility is recommended to be undertaken at an early stage in the scheme to confirm the requirements.

Soils may potentially be handled as Non-Waste and re-used on site (or on other sites) in accordance with various protocols such as those published by the EA or CL:AIRE. Typical requirements include:

- That the re-use of material will not endanger human health, cause nuisance, or harm the wider environment (controlled waters, ecosystems, etc.).
- That there is there a clear environmental benefit from the activity, and that the waste is being used as a substitute for non-waste material.
- The materials are suitable for use without further treatment.
- The holder is certain that the materials will be used in a safe manner.
- Only the necessary quantities of materials are being used.
- A Waste Recovery Plan (EA) or Materials Management Plan [MMP] (CL:AIRE) are produced and followed, and audited in a Verification Plan.

It may also be possible to treat materials under an environmental permit, standard rules permit, or U1 exemption, subject to strict limits.
The soil testing results from the MIR report suggests that the Made Ground is potentially suitable for re-use on site under hardstandings such as roads or slabs (subject to geotechnical considerations). The materials are not suitable for use in soft landscaped areas on account of being possibly physically unsuitable and locally (around HDTP2) exceeding the human health thresholds for PAH.

Records of the removal and disposal of soils must be kept and included within the final validation report. The records should include details of volumes, waste codes, facility that the material is sent to and dates etc.

4.4 Discovery Strategy

During groundworks, a watching brief is required by a competent environmental consultant, site-based engineer or site manager. Should visual signs or olfactory signs of unexpected contamination be identified then the following is required:

- Stop works in the location of identified gross contamination.
- Inform the Site Manager and Environmental Consultant.
- Environmental Consultant to inform Local Planning Authority Contaminated Land Team, with no further works undertaken in the area until any new recommendations have been agreed.
- Excavate the impacted area until impacted material is visually removed.
- The excavated material can be temporarily stockpiled on site, for pre-treatment and waste classification, prior to being disposed of offsite at a suitably licensed facility in accordance with the above (as detailed in Section 4.3.2).

Unexpected contamination may include:

- Visible fragments of asbestos board / tile or fibre (lagging);
- Soil headspace readings >100 ppm (using photo-ionisation detector [PID]);
- Significant discolouration of the soil;
- Visible hydrocarbon seeps; and,
- Strong hydrocarbon odour in the hand.

5.0 SITE CONTROLS

5.1 General Controls

Site works should be undertaken in accordance with the CDM:2015 Regulations and guidelines prepared by the Health and Safety Executive [HSE, 1991 Protection of Works and the General Public during the Development of Contaminated Land and Guidance Note HS(G)66, Health and Safety Executive, HMSO, 1991].

Detailed control measures with respect to contaminated land will be required during works on the site, to include (but not limited to):

- Monitoring of actual changes to ensure mitigation of potential adverse effects.
- Education of workers to risks associated with contamination (site inductions and appropriate toolbox talks).
- Posting of appropriate warning signs.
- Provision of suitable welfare facilities; and
- Provision of suitable PPE (and RPE if required).

5.2 Odours, Noise and Vibration

Care will need to be taken during activities to minimise the impact of any odours, dusts, noise and vibration on the surrounding buildings and receptors. In all instances, best practicable means (BPM) should be employed to control noise and vibration. BPM should also be employed to control dust emissions, such as (but not limited to) damping down dusty operations throughout the earthworks.

6.0 VALIDATION REPORT REQUIREMENTS

There is a requirement that the remediation of the site is validated and documented in line with Environment Agency document: verification of remediation of land contamination report (SC030114/RI).

The previous Main Investigation Report (21591) undertaken by Soils Limited identified some risks to receptors at the site and the following are recommended: -

- Excavating and disposing of poor quality soils (Made Ground) from the proposed soft landscaping areas and replacement with a capping system comprising imported topsoil / subsoil (minimum 150mm but dependent on type of vegetation to be grown).
- Waste Disposal considerations.
- A Discovery Strategy should also be followed during the development.

In line with the above remedial aspects, the Contractor will hold as a minimum:

- Records of all excavations including:
  - Ordnance survey extents and depths;
  - Photographic record of each excavation; and
  - Plans of the site showing where remediation has been undertaken including estimated area of each discrete soft landscaping area.
  - Records of the volume of each type of material excavated and imported to each remedial excavation / soft landscaping area will also be estimated and included in the Remediation Validation Report. There should be a calculation for soft landscaped areas to confirm the volume of material removed is the same as volume of imported soils.
  - Records of any changes to proposed changes to the landscaping scheme and changes to removed volumes of materials removed and imported.
- Records of laboratory analytical and *in-situ* field test results, including:
  - Laboratory test certificate for any verification test of imported material (subsoil and topsoil).
  - Particulars of remediation monitoring on site inspection sheets (date / location / personnel), the area of soft landscaping will be inspected to confirm depth and make up of 'clean' cover;
  - Calibration data for any field measurement equipment used during the remediation supervision in accordance with manufacturers guidance;
  - Confirmation of depths and volumes of each backfill layer; subsoil and topsoil layers; and,
  - Chain of custody forms.
- Records of any previously unidentified contamination, as detailed in the **Discovery Strategy** (if encountered). If any further remedial recommendations are required following completion of the various development phases (groundworks, landscaping etc.) a signed confirmation that the Discovery Strategy has been followed (including if no unexpected contamination was encountered) from the appointed site contractor or client will be required and copies included within the Remediation Validation Report.
- Records of material movement, including:
  - Volumes, origin and placement location of soils references to field results.

  - Details and quantities of excavated and imported materials.
  - Records of earthworks excavations including, as constructed, photographs, quantities of materials and records of progress; and,
  - Waste transfer notes for any material disposed of as waste.
- Waste classification and management documentation, including:
  - Details of all parties involved in the works.
  - Records of approval and method statements.
  - Records of discussions with regulatory authorities and written approval for actions.
  - Records of license applications (including mobile treatment license or declaration under the Definition of Waste Industry Code of Practice); and,
  - Records demonstrating environmental monitoring.

All relevant information as detailed in above shall be collected during the remediation works and an independent verification report complied on completion. The validation report shall take account of the recommendations in Land Contamination Risk Management (LCRM) Environment Agency 2020 and comprise as a minimum:

- A summary of the information contained in the risk assessment reports along with the agreed redevelopment strategy and objectives.
- Decision records covering agreement with regulators.
- Records of works undertaken and associated validation and monitoring records e.g. laboratory validation test certificates).
- Details of all parties involved in the works.
- Details and quantities of excavated soils and volumes disposed of off-site.
- Specialist contractor's validation reports for particular elements of work (if used).
- Details of the validation data for any imported soils used on-site (at least three sets of analyses per source) plus *in-situ* validation test results confirming depth and chemical quality.
- Waste classification and management documentation.
- Additional risks assessments / non-scheduled reactive works relating to previously unidentified contamination and all related remedial works that were undertaken; and,
- Final status of remediation and achievement remedial objectives to satisfy planning conditions.

It should be noted that consideration has not been given to the protection of groundworkers, during the construction phase of this project, as that is outside the scope of this report. Adequate protection measures should be provided within a Construction Method Statement, completed by the Principal Contractor (CDM regulations 2015) for the project.

REPORT CONDITIONS

The Client

This report may also be used only by the client named in section 1 and their appointed project team for the purpose of design, obtaining planning, building regulations approval, and in connection with finance. This report must not be used by any other persons or for other purposes without express written agreement of Land Science.

General

Land Science takes all reasonable professional care in preparation of this report, using current standards and industry practice. However, the evaluation of ground conditions depends on an interpretation and extrapolation of the conditions revealed by a limited data set. The level of risk is related to the extent of investigation and no site is ever free of risk. The client should understand their risks and liabilities. We accept no liability whatsoever in respect of:

- The scope, extent or design of an investigation.
- Any conditions not directly revealed by the investigation.
- Published standards or methodologies used or adopted in this report.
- The opinion of any other party including any regulator, authority or stakeholder.
- Any dispute, claim or consequential loss arising from any findings of this report.
- Third party information and data.

This report relates solely to ground-related matters as set out in the objectives and makes no representation on other matters such as ecology, arboriculture, invasive plant species, the condition of buildings and structures, hazardous building materials such as insulation or asbestos, the locations of boundaries, unexploded ordnance, and or planning constraints etc. Further reports should be commissioned in this respect as appropriate.

Regulators and Approvals

This (and any other) report should be submitted to relevant authorities for their own assessments and to provide their approval or comments accordingly. This should be in good time before commencing on site in case additional work is to be carried out.

Standards, technical guidance and regulatory positions change over time and which may therefore affect the findings and recommendations made in this report; this should be verified by the client prior to any critical project milestones. Where this information is used in design, the designer should verify that the information is appropriate and has been used correctly.

Variations with time

The report relates to conditions revealed at the time of the investigation and any monitoring visits. Some parameters may vary over time or seasonally; groundwater levels, ground gas compositions, or concentrations of contaminants are particularly variable in this respect. Further monitoring or verification should be considered as appropriate.

GLOSSARY OF TERMS

ACM	Asbestos Containing Material
BGS	British Geological Survey
BRE	Building Research Establishment
BS	British Standard
C4SL	Category 4 Screening Level
CBR	California Bearing Ratio
CDM	Construction Design and Management regulations
CIRIA	Construction Industry Research and Information Association
CL:AIRE	Contaminated Land: Applications in Real Environments
CLEA	Contaminated Land Exposure Assessment model
CSM	Conceptual Site Model
EA	Environment Agency
EQS	Environmental Quality Standards
FOC	Fraction of Organic Carbon
GAC	Generic Assessment Criterion
GQRA	Generic Quantitative Risk Assessment
mbgl	Meters Below Ground Level
NHBC	National House Building Council
mOD	Metres above Ordnance Datum
PAH's	Polycyclic Aromatic Hydrocarbons
PHE	Public Health England
PID	Photo-Ionisation Detector
PQRA	Preliminary Quantitative Risk Assessment
PSD	Particle Size Distribution Test
RMS	Remediation Method Statement
S4UL	Suitable for Use Level
SOM	Soil Organic Matter
SPZ	Source Protection Zone
SPT	Standard Penetration Test
SSSI	Sites of Special Scientific Interest
ST-WEL	Short Term Workplace Exposure Limit
SVOC's	Semi-Volatile Organic Compounds
TPH	Total Petroleum Hydrocarbons
TRRL / TRL	Transport Road Research Laboratory
TWA-WEL	Time Weighted Average Workplace Exposure Limit
UK HBF	United Kingdom House Building Federation
VOC's	Volatile Organic Compounds
WAC	Waste Acceptance Criteria

Contains public sector information licensed under the Open Government Licence v3.0 - http://www.nationalarchives.gov.uk/doc/open-government-licence/version/3



This document is the property of Land Science and is for their sole use only. If another party makes use of this document they must do so with Land Science's permission only.

Land Science	Title: Site Location		Reference: LS8077
	Project: Rowfold Lodge, Billingshurst, RH14 9DD		Figure: 1
	Client: Mr Rutherford		Date: 15/11/2024
	Prepared by: AL	Checked by: JM	Version: 0.1	Sheet: 1 of 1

www.landscience.co.uk
Telephone: 0345 604 6494

Unit 10, 19 Albert Drive, Burgess Hill, West Sussex, RH15 9TN
2nd Floor, 25-28 Field Street, London, WC1X 9DA

Contains public sector information licensed under the Open Government Licence v3.0 - http://www.nationalarchives.gov.uk/doc/open-government-licence/version/3



Legend

- Application boundary
- Window Sampler Borehole
- Hand Dug Trial Pit

All positions carried out by Soils Limited

This document is the property of Land Science and is for their sole use only. If another party makes use of this document they must do so with Land Science's permission only.

Land Science

Title: Exploratory Hole Plan			Reference: LS8077
Project: Rowfold Lodge, Billingshurst, RH14 9DD			Figure: 2
Client: Mr Rutherford			Date: 15/11/2024
Prepared by: AL	Checked by: JM	Version: 0.1	Sheet: 1 of 1

www.landscience.co.uk
Telephone: 0345 604 6494

Unit 10, 19 Albert Drive, Burgess Hill, West Sussex, RH15 9TN
2nd Floor, 25-28 Field Street, London, WC1X 9DA

Contains public sector information licensed under the Open Government Licence v3.0 - http://www.nationalarchives.gov.uk/doc/open-government-licence/version/3

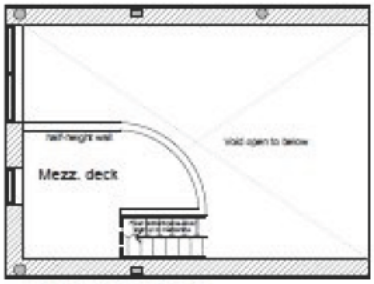

Mezzanine Storage area
(5.3m²)
(all head room above 1.5m)

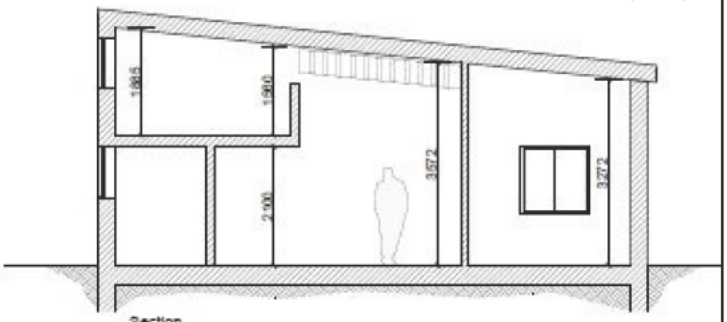



Ground Floor Plan
(37.2m²)

Total GIA 42.5m²
1bed 1 person

75% of ceilings 2.3m or above

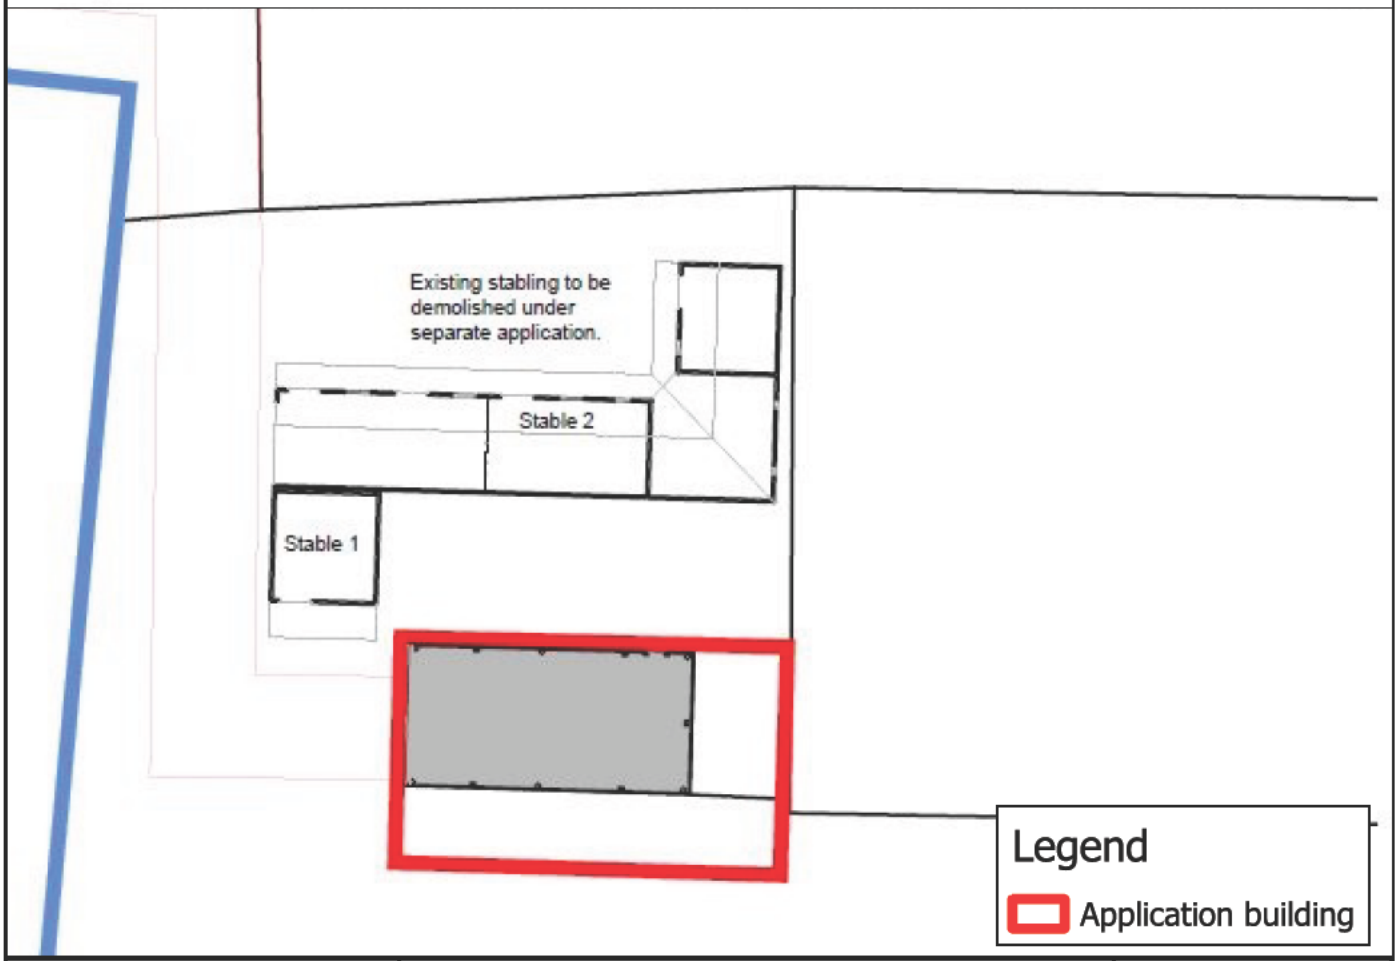

This document is the property of Land Science and is for their sole use only. If another party makes use of this document they must do so with Land Science's permission only.

Land Science	Title: Proposed Layout		Reference: LS8077
	Project: Rowfold Lodge, Billingshurst, RH14 9DD		Figure: 3
	Client: Mr Rutherford		Date: 15/11/2024
	Prepared by: AL	Checked by: JM	Version: 0.1 / Sheet: 1 of 1

www.landscience.co.uk
Telephone: 0345 604 6494

Unit 10, 19 Albert Drive, Burgess Hill, West Sussex, RH15 9TN
2nd Floor, 25-28 Field Street, London, WC1X 9DA

APPENDIX A

TERRAM
Hi Vis Geotextile



TERRAM Hi Vis is a non-woven orange geotextile used for separating contaminated/uncontaminated soils.

TERRAM Hi Vis geotextiles have a dual effect:
its vivid colour warns of potential danger at the point of any future excavations and it can also prevent the upward movement of contaminated soil particles.

Preventing intermixing of granular materials and soils

TERRAM Hi Vis geotextiles provide an effective solution to the problem of constructing a stable granular layer over soft foundation soils. When stone is placed directly on a soft subgrade, the imposed load often causes intermixing of two layers. This results in contamination of the stone layer and a resulting loss in bearing strength, surface rutting and deformation at the sub-base/subgrade interface.

Preventing the ingress of fines into drainage media

Whether it's a granular drain or a geosynthetic alternative such as open geocellular units, TERRAM Hi Vis geotextiles are ideal for preventing the ingress of fines.

TERRAM filters/separators are used extensively in the construction of

- Paved and unpaved roads
- Railways
- Car parks and hardstandings
- Cycleways and footpaths
- SuDS installations
- Green roofs

Features

- Engineered to provide high strength and high elongation at break
- Manufactured from high tenacity UV stabilised virgin polypropylene fibres to provide long term durability in all soil types
- Manufactured using a randomly orientated web to provide completely isotropic properties
- Excellent uniformity with high permeability and low pore size for soil filtration

PRODUCT GRADE	T1000 Orange Geotextile
Roll Width (*) m	4.5/6
Roll Length (*) m	100

TERRAM product specifications can be downloaded from **www.terram.com**

APPENDIX B

TIER 1 SOIL SCREENING (HUMAN HEALTH)

Project:	Rowfold Lodge	**Soil Organic Matter (calculated):**	0.33%
Reference:	LS8077	**Soil Organic Matter (adopted):**	1.00%
Assessor:	JM	**Scenario:**	Residential (with vegetation)

Lab Sample Ref.	
Location Ref.	
Depth (m)	
Sample Number	
Date sample taken	
Time sample taken	

Determinand	Source	Value	Units	Detection Limit
Asbestos (Identification)	N/A	Not-detected	Type	N/A
Herbicide and Pesticide Screening	N/A	Absent	P/A	-
General Inorganics				
pH	NONE	-	pH Units	N/A
Total Cyanide	NONE	-	mg/kg	1
Water Soluble Sulphate (Soil Equivalent)	No health risk	-	g/l	-
Water Soluble Sulphate as SO_4 (2:1)	No health risk	-	mg/kg	-
Water Soluble Sulphate (2:1 Leachate Equivalent)	No health risk	-	g/l	0.00125
Sulphide	NONE	-	mg/kg	1
Fraction Organic Carbon (FOC)	No health risk	-	N/A	0.001
Total Organic Carbon (TOC)	No health risk	-	%	0.1
Loss on Ignition @ 450oC	NONE	-	%	0.2
Acid Neutralisation Capacity	No health risk	-	+/- mol/kg	-100
Total Phenol				
Total Phenol (monohydric)	S4UL	120	mg/kg	1
Speciated PAHs				
Naphthalene	S4UL	2.3	mg/kg	0.05
Acenaphthylene	S4UL	170	mg/kg	0.1
Acenaphthene	S4UL	210	mg/kg	0.1
Fluorene	S4UL	170	mg/kg	0.1
Phenanthrene	S4UL	95	mg/kg	0.1
Anthracene	S4UL	2400	mg/kg	0.1
Fluoranthene	S4UL	170	mg/kg	0.1
Pyrene	S4UL	620	mg/kg	0.1
Benzo(a)anthracene	S4UL	7.2	mg/kg	0.1
Chrysene	S4UL	15	mg/kg	0.05
Benzo(b)fluoranthene	S4UL	2.6	mg/kg	0.1
Benzo(k)fluoranthene	S4UL	77	mg/kg	0.1
Benzo(a)pyrene	S4UL	2.2	mg/kg	0.1
Indeno(1,2,3-cd)pyrene	S4UL	27	mg/kg	0.1
Di-benzo(a,h)anthracene	S4UL	0.24	mg/kg	0.1
Benzo(ghi)perylene	S4UL	320	mg/kg	0.05

Coronene	NONE	-	mg/kg	0.05
Total PAHs				
Total WAC-17 PAHs	NONE	-	mg/kg	1.6
Heavy Metals / Metalloids				
Arsenic	S4UL	37	mg/kg	1
Barium	NONE	-	mg/kg	1
Beryllium	S4UL	1.7	mg/kg	0.06
Boron	S4UL	290	mg/kg	0.2
Cadmium	S4UL	11	mg/kg	0.2
Chromium (VI)	S4UL	6	mg/kg	-
Chromium (III)	S4UL	910	mg/kg	1
Copper	S4UL	2400	mg/kg	1
Lead	C4SL	200	mg/kg	1
Mercury (elemental)	S4UL	1.2	mg/kg	0.3
Mercury (Inorganic)	S4UL	40	mg/kg	0.3
Mercury (Methylmercury)	S4UL	11	mg/kg	0.3
Nickel	S4UL	130	mg/kg	1
Selenium	S4UL	250	mg/kg	1
Vanadium	S4UL	410	mg/kg	1
Zinc	S4UL	3700	mg/kg	1
Monoaromatics				
Benzene	S4UL	87	µg/kg	1
Toluene	S4UL	130000	µg/kg	1
Ethylbenzene	S4UL	47000	µg/kg	1
Xylene (p & m) [note - values for p used]	S4UL	56000	µg/kg	1
Xylene (o)	S4UL	60000	µg/kg	1
MTBE (Methyl Tertiary Butyl Ether)	NONE*	1	µg/kg	1
Total BTEX	NONE		µg/kg	10
